



Action and Task Progress Report- Standard




Waikato District Council

camms**strategy**

Print Date: 15-Jun-2023

BREAKDOWN BLUEPRINT PLAN

	All	Council-led	Community-led
Initiatives Not Started	174	116	58
Initiatives In Progress	115	104	11
Initiatives Ongoing	19	16	3
Initiatives Completed	29	27	2
Initiatives Deferred	3	2	1
Total	340	265	75

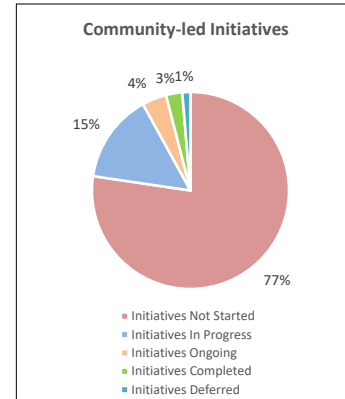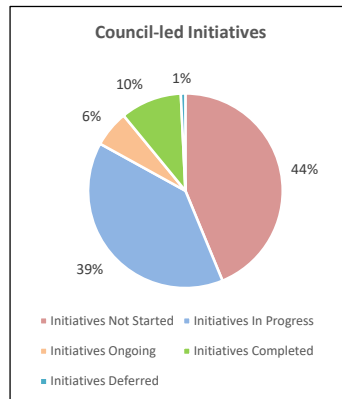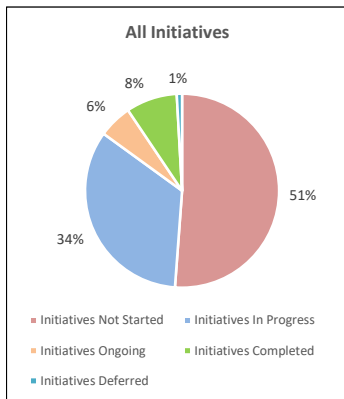

BREAKDOWN BY AREA

By Area	Not Started	In Progress	Ongoing	Completed	Deferred	Total
Gordonton	24	2	0	0	0	26
Port Waikato	32	1	0	0	0	33
Raglan	10	7	3	1	0	21
Te Kauwhata	8	8	1	0	0	17
Te Kowhai	4	5	0	2	0	11
Tamahere	4	6	2	3	0	15
Taupiri	9	5	0	0	0	14
Tuakau	8	3	2	7	0	20
Whatawhata	7	3	2	7	0	19
District Wide	21	26	6	8	0	61
Horotiu	5	4	1	1	2	13
Huntly	9	5	1	0	0	15
Matangi	2	6	0	1	0	9
Mercer	8	2	0	0	0	10
Meremere	5	8	2	0	0	15
Ngaruawahia	9	8	0	1	0	18
Ohinewai	6	7	0	2	1	16
Pokeno	3	7	1	2	0	13
Total	174	113	21	35	3	346

2.1 Gordonton

2.1.1 Communities

Action Title: 9.1.5.282 GN4.1 Continue to redevelop Hukanui Park with a playground, seating and possible other recreation facilities, while ensuring the history of the heritage buildings in and around the park is celebrated, as well as iwi cultural aspects, considering local reserve status, infrastructure limitations, and Building Code requirements.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	24-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 24-Aug-2022

Action Title: 9.1.5.283 GN4.2 Facilitate the re-establishment of the markets:

- Facilitate organisational arrangements
- Provide infrastructure to accommodate traffic and parking.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	24-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 24-Aug-2022

Action Title: 9.1.5.284 GN4.3 Improve the safety and security of commercial areas and within community, considering CCTV, increased surveillance, neighbourhood watch etc.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	24-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 24-Aug-2022

Action Title: 9.1.5.285 GN4.4 Install public recycle bins by the public toilets.

Responsible Person	Status	Start Date	End Date	% Complete
Phillip Ellis - Solid Waste Team Leader	Not Started	25-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 25-Aug-2022

Action Title: 9.1.5.286 GN4.5 Support the churches with expertise and advice on matters regarding earthquake strengthening.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	25-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 25-Aug-2022

Action Title: 9.1.5.287 GN4.6 Provide a sports facility, possibly in conjunction with the current facilities in the Domain or elsewhere.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	25-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 25-Aug-2022</i>				

Action Title: 9.1.5.288 GN4.7 Investigate the need for improvements to the cemetery, consider:

- Parking issues
- Wetland and native trees
- A shared path from the cemetery to Woodlands Road
- Traffic safety.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	25-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 25-Aug-2022</i>				

2.1.2 Economy

Action Title: 9.1.5.289 GN6.1 Produce and implement a business attraction strategy to encourage the development of appropriate commercial activities.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	25-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 25-Aug-2022</i>				

2.1.3 Governance

Action Title: 9.1.5.290 GN9.1 Recognise or clarify the role of the Gordonton Community Committee and improve communication between the community and the Council.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	25-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 25-Aug-2022</i>				

Action Title: 9.1.5.291 GN9.2 Assist community-led initiatives where the Council can give support, e.g. building on arts and culture sector to strengthen identity.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	25-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 25-Aug-2022</i>				

2.1.4 Growth

Action Title: 9.1.5.292 GN5.1 Identify if, how much, and where, possible additional residential and commercial land beyond the existing zoning could be located and what this means for infrastructure and the role and design of

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	25-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				

Action Title: 9.1.5.293 GN5.2 Investigate with the landowner the possible barriers for the development of the residential zoned land by the school and remove these barriers if within the Council's control.

Responsible Person	Status	Start Date	End Date	% Complete
Will Gauntlett - Growth and Analytics Manager	Not Started	25-Aug-2022	30-Jun-2023	0%

Action Progress Comments: New project - not yet allocated to a staff member.
Last Updated: 18-Apr-2023

2.1.5 Identity

Action Title: 9.1.5.294 GN1.1 Produce an identity strategy for Gordonton.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	25-Aug-2022	30-Jun-2023	0%

Action Progress Comments:
Last Updated: 25-Aug-2022

2.1.6 Infrastructure

Action Title: 9.1.5.295 GN8.1 Improve streetlights in the village centre, considering solar power or LED.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:
Last Updated: 26-Aug-2022

Action Title: 9.1.5.296 GN8.2 Promote the installation of a wastewater system for Gordonton in subregional planning programmes.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:
Last Updated: 26-Aug-2022

Action Title: 9.1.5.297 GN8.3 Advocate for better internet connectivity.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:
Last Updated: 26-Aug-2022

2.1.7 Iwi

Action Title: 9.1.5.298 GN3.1 Improve the relationships between WDC and local mana whenua.

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	In Progress	26-Aug-2022	30-Jun-2023	1%

Action Progress Comments: Our PIH team have been working hard, specifically over the last three years to improve our relationships with Mana whenua. We are trying to improve these relationships by engaging early and inviting
Last Updated: 30-May-2023

Action Title: 9.1.5.299 GN3.2 Engage and collaborate with iwi regarding cultural interpretation signage within public realm projects.

Responsible Person	Status	Start Date	End Date	% Complete
Nghina Armstrong-Nield - Iwi and Community Partnerships Advisor	In Progress	26-Aug-2022	30-Jun-2023	1%

Action Progress Comments: I think we as Council are improving in this space. We have engaged and collaborated with local Mana whenua when undertaking projects for help with designing and producing cultural references. We are
Last Updated: 30-May-2023

2.1.8 Nature

Action Title: 9.1.5.300 GN2.1 Plant more trees in and around the village and establish riparian planting and a nature trail.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 26-Aug-2022

Action Title: 9.1.5.301 GN2.2 Develop the land behind St Mary's Church as wetland and bring it back into its natural state (while working with the marae).

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 26-Aug-2022

2.1.9 Transport

Action Title: 9.1.5.302 GN7.1 Continue with plans to improve the amenity of Gordonton Road as part of the revocation, including lower speed limit, traffic visibility around Woodlands Road, safer crossings and connections, safety conditions and beautification of entrances to the village (more detail in action description).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 26-Aug-2022

Action Title: 9.1.5.303 GN7.2 Continue with the upgrade of College Drive with footpaths and lighting, and provide a timeframe for these works.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:

Last Updated: 26-Aug-2022

Action Title: 9.1.5.304 GN7.3 Build a shared path along the Komakorau Stream connecting Taupiri, Woodlands Estate, the village centre to Wairere nurseries and Hukanui Marae.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:*Last Updated: 26-Aug-2022*

Action Title: 9.1.5.305 GN7.4 Consider traffic issues around Gordonton School by investigating whether:

- More parking is required
- More space for buses is needed
- The narrow footpath along the one-lane bridge needs widening
- More and safer crossings on Woodlands Road are needed.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:*Last Updated: 26-Aug-2022*

Action Title: 9.1.5.306 GN7.5 Advocate to Waikato Regional Council for public transport services to Gordonton.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:*Last Updated: 26-Aug-2022*

Action Title: 9.1.5.307 GN7.6 Investigate the feasibility of the upgrade of Peach Road and installation of footpaths to increase the safety of pedestrians and cyclists along this narrow road that is increasingly being used.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%

Action Progress Comments:*Last Updated: 26-Aug-2022*

2.10 Port Waikato

2.10.1 Communities

Action Title: 9.1.5.308 PW4.1 Continue the planned construction and/or upgrades of playgrounds at Cobourne Reserve, Maraetai Bay, and Cordyline Road / Phillips Reserve.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: <i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.309 PW4.2 Redevelop the wharf area:

Responsible Person	Status	Start Date	End Date	% Complete
Patrick Edwards - Contractor - Capex Delivery Consultant	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: <i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.310 PW4.3 Improve the trailer parking around the existing second boat ramp to encourage its use and relieve the pressure on the boat ramp in the wharf area.

Responsible Person	Status	Start Date	End Date	% Complete
Patrick Edwards - Contractor - Capex Delivery Consultant	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: <i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.311 PW4.4 Improve general safety:

- Increase of police presence at events, long weekends, holiday periods
- Reinstatement of neighbourhood street co-ordinators with direct lines of communication.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: <i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.312 PW4.5 Facilitate the provision of a library book service in Port Waikato.

Responsible Person	Status	Start Date	End Date	% Complete
Shelby Spain - Customer Delivery Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: This initiative has not been progressed. This will be investigated to see how we can deliver this service to be consistent. Click and collect has been initiated in the last 12 months across all libraries, available <i>Last Updated: 26-May-2023</i>				

Action Title: 9.1.5.313 PW4.6 Consider options for the future of the public tennis court and the basketball half-court, considering the establishment of a youth hub with a skate and scooter park, mountain bike tracks, BMX course etc.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.314 PW4.7 Provide a regularly updated list of service providers for our community, aside from the Port Report.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.315 PW4.8 Increase opportunities for recycling, e.g. through a large organic waste bin, a local recycling centre, inorganic collection etc.

Responsible Person	Status	Start Date	End Date	% Complete
Phillip Ellis - Solid Waste Team Leader	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.316 PW4.9 Prepare a concept plan for improvements to Cobourne Reserve, considering:

- Increasing planting
- Adding lighting at carpark
- Providing wheelchair access.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.317 PW4.10 Establish a community garden.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.10.2 Economy

Action Title: 9.1.5.318 PW6.1 Increase local services zoned land to provide opportunities for commercial activities and local employment, e.g. shops, retail, restaurants.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.319 PW6.2 Promote existing and attract more hospitality services and businesses.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.10.3 Governance

Action Title: 9.1.5.320 PW9.1 Improve support to community-led initiatives and communication between Council and the community, and invite community-led initiatives where the Council can give support; possible ideas:

- Build on Arts and Culture to strengthen Identity, e.g. through events
- Activities by 'Friends of Cobourne Reserve'.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: April 2023:				
<i>Last Updated: 02-Jun-2023</i>				

Action Title: 9.1.5.321 PW9.2 Strengthen the relationship and communication between the Port Waikato Residents and Ratepayers Association and the Community Board.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments: April 2023:				
<i>Last Updated: 02-Jun-2023</i>				

2.10.4 Identity

Action Title: 9.1.5.322 PW1.1 Undertake a public realm upgrade at the wharf area to make a gateway statement and address the lack of gathering space, considering:

- Seating
- Public art (both contemporary and reflective of the area's significance for mana whenua)
- A boardwalk connection with Cobourne Reserve
- Wayfinding and orientation signage
- Signage showing the Wharf, Cobourne Reserve, possibly other areas, with information on the history.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.323 PW1.2 Produce an identity strategy for Port Waikato.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.10.5 Infrastructure

Action Title: 9.1.5.324 PW8.1 Continue the public toilet upgrade and relocation at Sunset Beach.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.325 PW8.2 Improve stormwater management and especially address drainage issues along Maunsell Road and Centreway Road.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.326 PW8.3 Improve street lighting, considering solar power or LED.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.327 PW8.4 Upgrade public toilets and their wastewater disposal at Maraetai Bay.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.328 PW8.5 Investigate the installation of commercial wastewater treatment and water supply for inclusion in the Asset Management Plan to encourage growth and commercial development, especially in the Wharf and Sunset Beach areas.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.10.6 Iwi

Action Title: 9.1.5.329 PW3.1 Erect signage to mark and explain the history and cultural significance for mana whenua of the following:

- The wetland
- The marae and the ownership of the land gifted to the mission
- The whale graveyard
- The Pa site on the hill, which also needs to be connected with a walkway
- Events related to Te Tiriti.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.330 PW3.2 Resolve access issues across the recreation reserve in Ashwell Drive.				
Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.331 PW3.3 Improve the relationships between WDC, the local community committee, and local mana whenua.				
Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.10.7 Nature

Action Title: 9.1.5.332 PW2.1 Continue the erosion / resilience planning project, including regular clean-ups of debris, and provide ongoing clarity on what is being done.				
Responsible Person	Status	Start Date	End Date	% Complete
Jim Ebenhoh - Planning and Policy Manager	In Progress	26-Aug-2022	30-Jun-2023	25%
Action Progress Comments: After completion of necessary technical reports, recent focus has been on short-term options to slow coastal erosion, such as sand push-ups. A scoping exercise is being done at present that is likely to				
<i>Last Updated: 25-May-2023</i>				

Action Title: 9.1.5.333 PW2.2 Improve litter control in the summer peak months, e.g. by increasing the frequency of servicing the public rubbish bins, providing separated bins, no-litter signs, no-freedom camping signs, and clean-up of public areas.				
Responsible Person	Status	Start Date	End Date	% Complete
Phillip Ellis - Solid Waste Team Leader	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.334 PW2.3 Advocate for ecological improvements in the wetland area.				
Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.335 PW2.4 Along with Waikato Regional Council and Department of Conservation, support the community's restoration and weed control initiatives in the sand dune areas.				
--	--	--	--	--

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.10.8 Transport

Action Title: 9.1.5.336 PW7.1 Continue to maintain the entry road into Port Waikato in light of erosion and subsidence.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.337 PW7.2 Improve road safety in response to speeding and antisocial behaviour on roads, the beach and in the dunes, e.g. through more speed limit signs, cameras, police presence, speed bumps, especially along Maunsell Road and at Maraetai Bay Reserve.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.338 PW7.3 Improve the pedestrian safety and traffic management at the Sunset Beach carpark, especially considering parking manoeuvring.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.339 PW7.4 Advocate to Waikato Regional Council for shuttle services to key facilities and / or higher frequency public transport services to Port Waikato e.g. on the weekends and on Thursdays.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

Action Title: 9.1.5.340 PW7.5 Develop more recreational walkways and connect cycling destinations through tracks and cycle lanes.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	26-Aug-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 26-Aug-2022</i>				

2.11 Raglan

2.11.1 Communities

Action Title: 9.1.5.134 RA4.1 Extend free wi-fi around the library.

Responsible Person	Status	Start Date	End Date	% Complete
Shelby Spain - Customer Delivery Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: We haven't had any request to extend.

Last Updated: 26-May-2023

Action Title: 9.1.5.135 RA4.2 Support the Whaingaroa Raglan Affordability Project.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Dec-2021

Action Title: 9.1.5.136 RA4.3 Support entities undertaking youth social initiatives.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

Action Title: 9.1.5.137 RA4.4 Support the development of a community hub for locals, youth skills, cultural, health and wellbeing and environmental exchange (OMG Tech). Consider the Wi Neera Street old surgery' building (1) as an option.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Dec-2021

Action Title: 9.1.5.138 RA4.5 Investigate the development of a recreation centre [and pool] and bringing sports together.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Budget allocated to refurbish Raglan Rugby Club Rooms next FY. Local developer has also indicated that they may develop a community pool which will be held in private ownership.

Last Updated: 01-Jun-2022

2.11.2 Economy

Action Title: 9.1.5.139 RA6.1 Support initiatives by the tech and visitor sectors to address youth unemployment.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Action Title: 9.1.5.140 RA6.2 Promote the formation of a business hub for high tech promotion and exchange.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 15-Dec-2021

Action Title: 9.1.5.141 RA6.3 Consider how to support the community in creating additional and sustaining existing local jobs in tourism. Consider a bed tax to compensate for increased waste and to support housing affordability initiatives.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	5%

Action Progress Comments: Project - Reigniting Tourism in Raglan – Creating a new look tourism sector that is self-sustaining and thriving, that promotes our unique identity while celebrating our people, our stories and our place.

Last Updated: 26-May-2022

Action Title: 9.1.5.142 RA6.4 Investigate opportunities for short-stay courses.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 15-Dec-2021

Action Title: 9.1.5.143 RA6.5 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the

Last Updated: 30-May-2023

Action Title: 9.1.5.144 RA6.6 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the

Last Updated: 30-May-2023

2.11.3 Governance

Action Title: 9.1.5.148 RA9.1 Investigate whether Harbour Board income is used locally (2).

Responsible Person	Status	Start Date	End Date	% Complete
Nick Johnston - Advocacy and Investment Advisor	Completed	01-Jul-2021	30-Jun-2024	100%

Action Progress Comments:

Action Title: 9.1.5.149 RA9.2 Partner with Raglan Naturally in respect to planning processes.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Ongoing	01-Jul-2021	30-Jun-2022	-0%

Action Progress Comments: There are currently no planning processes specifically related to Raglan, but when the time arises, Raglan Naturally will be included.

Last Updated: 17-May-2022

2.11.4 Identity

Action Title: 9.1.5.130 RA1.1 Build on the strong identity of Raglan based on the unique qualities of the local area (refer to DW1.2 to 1.4). Consider nature, regeneration, environmental initiatives, the arts, and surfing.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	5%

Action Progress Comments: Project - Reigniting Tourism in Raglan – Creating a new look tourism sector that is self-sustaining and thriving, that promotes our unique identity while celebrating our people, our stories and our place.

Last Updated: 26-May-2022

2.11.5 Iwi

Action Title: 9.1.5.133 RA3.1 Support a strong Maaori culture, including education on the Treaty of Waitangi, respecting tangata whenua, and creating Te Reo signage (refer to DW3.3).

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	In Progress	01-Jul-2021	30-Jun-2024	1%

Action Progress Comments:

Last Updated: 30-May-2023

2.11.6 Nature

Action Title: 9.1.5.131 RA2.1 Support Raglan Naturally in their prioritised local initiatives such as local food production, energy self sufficiency, alternatives to weed spraying, GE free approaches and education regarding climate change.

Responsible Person	Status	Start Date	End Date	% Complete
Rachael Goddard - Climate Action and Sustainability Manager	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: Ongoing support offered to Raglan Naturally in community-led development. The Climate Action & Sustainability Manager sits on the board of Raglan Naturally in a personal capacity. Raglan Naturally and

Last Updated: 30-May-2023

Action Title: 9.1.5.132 RA2.2 Support community in Zero Waste initiatives, spread learning across the district.

Responsible Person	Status	Start Date	End Date	% Complete
Rachael Goddard - Climate Action and Sustainability Manager	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: The Climate Action & Sustainability Manager is providing support and input via the WDC Waste Minimisation Steering Group. Support has also been offered externally to Xtreme Zero Waste via the Climate

Last Updated: 24-May-2023

2.11.7 Transport

Action Title: 9.1.5.145 RA7.1 Extend walking and cycling network, including to Whale Bay.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jun-2022	30-Sep-2022	30%
Action Progress Comments: UNDERWAY - WALE BAY IS UNLIKELY TO PROCEED DUE TO HAPU LAND CLAIM				
<i>Last Updated: 01-Jun-2023</i>				

Action Title: 9.1.5.146 RA7.2 Improve traffic safety around the school.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jan-2022	30-Aug-2024	30%
Action Progress Comments: speed limits changed as part of speed bylaw 2021 - school zones created				
<i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.147 RA7.3 Develop a parking strategy.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2022	30-Jun-2023	0%
Action Progress Comments:				
<i>Last Updated: 15-Dec-2021</i>				

2.11.8 Other

Action Title: 9.1.5.150 RA10.1 Raglan Naturally suggestions for LTP beyond Blueprint.

Responsible Person	Status	Start Date	End Date	% Complete
Nicole Hubbard - Corporate Planning Manager	Not Started	01-Jul-2021	30-Jun-2022	0%
Action Progress Comments: No action has been taken as yet. This will form part of the LTP 2024 project considerations. The project is anticipated to commence 1 July 2022 however projects will not be consider until 2023.				
<i>Last Updated: 06-May-2022</i>				

2.12 Te Kauwhata

2.12.1 Communities

Action Title: 9.1.5.153 TK4.1 Work with the Ministry of Education to agree an integrated approach to delivering additional educational capacity, especially where associated with new residential areas (1).

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 17-Dec-2021

Action Title: 9.1.5.154 TK4.2 Promote the provision of health services.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	1%

Action Progress Comments: Community house alongside the health centre lead this.

Last Updated: 26-May-2022

Action Title: 9.1.5.155 TK4.3 Consider the provision of facilities to accommodate community, and active and passive recreational activities.

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	In Progress	01-Jul-2021	30-Jun-2024	20%

Action Progress Comments: Community committee has assigned funding support person to assist with funding for 4 projects at the Te Kauwhata Domain. Currently scoping progress with project leaders. Connecting to Open space s

Last Updated: 22-Aug-2022

2.12.2 Economy

Action Title: 9.1.5.158 TK6.1 Consider rezoning the site of the existing primary school as commercial to allow for a central business hub (in conjunction with the initiative to identify additional educational facilities elsewhere, see TK4.1).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Ongoing	01-Jul-2021	30-Jun-2022	-0%

Action Progress Comments: Waikato 2070 identifies this site as an area for possible future expansion for the town centre. No change in the land use is able to take place until such time that the site is no longer designated for schooling

Last Updated: 22-Aug-2022

Action Title: 9.1.5.159 TK6.2 Determine key town centre strategy and management needs.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2021	30-Jun-2022	0%

Action Progress Comments: Town Centre Plans have been prioritised for Pokeno, Huntly and Ngaruawahia. Priority could be considered as part of the 2024-2034 Long Term Plan.

Last Updated: 30-May-2023

Action Title: 9.1.5.160 TK6.3 Strengthen and emphasise linkages to the Waikato River and the Te Araroa Trail, and leverage for tourism.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Rebecca Law - Reserves Planner	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: No progress has been made on this. The ramparts and trenches that formed the core of the Rangiriri Pa's defences are ready, and the reconstructed North Waikato pa formally re-opened on 23 April 2022				
<i>Last Updated: 17-May-2022</i>				

Action Title: 9.1.5.161 TK6.4 Provide a covered facility to accommodate the markets.

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not currently planned or budgeted for. Potential opportunity to identify the need with local developers and could be incorporated into future plans.				
<i>Last Updated: 12-May-2023</i>				

Action Title: 9.1.5.162 TK6.5 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%
Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the				
<i>Last Updated: 30-May-2023</i>				

Action Title: 9.1.5.163 TK6.6 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%
Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the				
<i>Last Updated: 30-May-2023</i>				

2.12.3 Growth

Action Title: 9.1.5.156 TK5.1 Consider measures to ensure high quality new residential environments.

Responsible Person	Status	Start Date	End Date	% Complete
Sandra Kelly - Programme Manager District Plan	In Progress	01-Jul-2021	30-Jun-2023	5%
Action Progress Comments: No action as appeals work and Variation 3 are the main priority for the team at present.				
<i>Last Updated: 30-May-2023</i>				

Action Title: 9.1.5.157 TK5.2 Provide design guidance to ensure housing diversity for different family sizes.

Responsible Person	Status	Start Date	End Date	% Complete
Sandra Kelly - Programme Manager District Plan	In Progress	01-Jul-2021	30-Jun-2023	5%
Action Progress Comments: No progress as appeals and variation 3 are the priority for the team.				
<i>Last Updated: 30-May-2023</i>				

2.12.4 Identity

Action Title: 9.1.5.151 TK1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Te Kauwhata, consider viticultural history, Lake Waikare, and the Whangamarino wetlands. Develop a heritage trail highlighting the viticultural history of Te Kauwhata.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not yet started				
<i>Last Updated: 02-Jun-2023</i>				

Action Title: 9.1.5.152 TK1.2 Promote Rangiriri, highlighting the area's history.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: not yet started				
<i>Last Updated: 02-Jun-2023</i>				

2.12.5 Transport

Action Title: 9.1.5.164 TK7.1 Produce a cycling and walking strategy to develop local connections and paths, including around the lakes and the Whangamarino Wetland.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	25%
Action Progress Comments: The WDC trails strategy is under review and will be consulted on, as the Connectivity Strategy to include all connections - trails, footpaths, cycle trails, bridle trails etc. Content review and drafting of new				
<i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.165 TK7.2 Consider alternatives to the bypass that achieves the aims of reducing trucks through the village (2).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jun-2022	30-Jun-2023	5%
Action Progress Comments: planning underway				
<i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.166 TK7.3 Consider facilitating a grade-separated rail crossing, at existing or possible bypass location (3).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: not planned in the LTP				
<i>Last Updated: 02-Jun-2022</i>				

2.12.6 Other

Action Title: 9.1.5.167 TK8.1 New initiative: Main street / town centre pedestrian and traffic safety measures.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	02-Oct-2024	30-Jun-2026	0%
Action Progress Comments: TO BE CONSIDERED IN THE NEXT LTP				
<i>Last Updated: 02-Jun-2022</i>				

2.13 Te Kowhai

2.13.1 Communities

Action Title: 9.1.5.169 TE4.1 Facilitate school expansion by shared use of the sportsfields or moving the fields to a new site (1).

Responsible Person	Status	Start Date	End Date	% Complete
Megan May - Acting General Manager - Service Delivery	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: School have a walkway to the village green fields and have use of it at all times.

Last Updated: 01-Jun-2022

Action Title: 9.1.5.170 TE4.2 Create a village green by expanding sports fields and include changing rooms and public toilets (2).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	15%

Action Progress Comments: Negotiations are currently underway to purchase land within the Te Kowhai area. If successful, this purchase will cover future of growth in this area until 2040.

Last Updated: 01-Jun-2022

2.13.2 Economy

Action Title: 9.1.5.171 TE6.1 Support the expansion or intensification of the airpark with commercial uses associated with aeronautical activities (3).

Responsible Person	Status	Start Date	End Date	% Complete
Sandra Kelly - Programme Manager District Plan	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The Proposed District Plan Decision allows for the expansion and aeronautical development in Te Kowhai.

Last Updated: 17-May-2022

Action Title: 9.1.5.172 TE6.2 Consider expanding commercial zone towards garage (4).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.173 TE6.3 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.174 TE6.4 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%
Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).				
<i>Last Updated: 30-May-2023</i>				

2.13.3 Identity

Action Title: 9.1.5.168 TE1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Te Kowhai, consider the airpark.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not yet started				
<i>Last Updated: 26-May-2022</i>				

2.13.4 Transport

Action Title: 9.1.5.175 TE7.1 Support the development of a new inner relief road, connecting Horotiu Road and Te Kowhai Road (5).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: will be developed as part of structure planning and developer growth cells- next ltp				
<i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.176 TE7.2 Support the expansion of the footpath network in new residential developments and connecting to the village centre.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: to be developed as part of the next LTP, programme for this year is full				
<i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.177 TE7.3 Support the completion of the Te Otamanui walkway by the community.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	25%
Action Progress Comments: \$20,000 allocated per annum through the LTP to support the Te Kowhai Community Group in completing the Te Otamanui Walkway				
<i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.178 TE7.4 Provide longer distance walking and cycling connections from the Te Otamanui walkway along the Waipa River to Ngaruawahia (also refer to DW1.3).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: to be developed as part of the next LTP, programme for this ltp is full				
<i>Last Updated: 02-Jun-2022</i>				

2.14 Tamahere

2.14.1 Communities

Action Title: 9.1.5.181 TM4.1 Support the Zero Waste initiative at the Hub as a start of possible wider local initiative.

Responsible Person	Status	Start Date	End Date	% Complete
Phillip Ellis - Solid Waste Team Leader	In Progress	01-Jul-2021	30-Jun-2024	20%

Action Progress Comments: Project on hold due to unplanned key staff member exit. Replacement starts mid June and will pick this up again

Last Updated: 25-May-2022

2.14.2 Economy

Action Title: 9.1.5.183 TM6.1 Support activation of the Hub development (3).

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Need regular events.

Last Updated: 08-Dec-2022

Action Title: 9.1.5.184 TM6.2 Support local employment initiatives. Consider the quarry (needs commercial rights), elderly housing, leveraging off cycle route, retail in the new commercial hub, Southern Fresh Foods, home-based employment etc.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 21-Dec-2021

Action Title: 9.1.5.185 TM6.3 Facilitate a plan to rotate the location of the local markets between the current location at the church and the reserve in Matangi in order to increase frequency (4).

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Cr Beavis comment: unrealistic as not how markets operate.

Last Updated: 14-Jun-2023

Action Title: 9.1.5.186 TM6.4 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	5%

Action Progress Comments: Consideration for employment land (Industrial, Town Centre, Commercial and Local Centre zones) beyond the zoning in the Proposed District Plan Decisions is work that needs to be undertaken. This work

Last Updated: 17-May-2022

Action Title: 9.1.5.187 TM6.5 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	5%

Action Progress Comments: Consideration for employment land (Industrial, Town Centre, Commercial and Local Centre zones) beyond the zoning in the Proposed District Plan Decisions is work that needs to be undertaken. This work will be informed by a demand and supply assessment at a sub-regional partnership level.

Last Updated: 17-May-2022

2.14.3 Growth

Action Title: 9.1.5.182 TM5.1 Investigate whether the land bounded by SH21, Tamahere Drive and the proposed southern links route should be rezoned from rural to Village (2).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Council have taken a strong position on providing for no more Rural Residential or Large Lot Residential development in the District.

Last Updated: 17-May-2022

2.14.4 Identity

Action Title: 9.1.5.179 TM1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Tamahere, consider the gully network, Wiremu Tamihana (celebrating heritage), and the markets.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Cr Beavis: someone looking at Tamahere heritage sign for piazza and church (with funding available) but keen on proposed heritage sign for the Narrows.

Last Updated: 14-Jun-2023

2.14.5 Nature

Action Title: 9.1.5.180 TM2.1 Support Mangaone Stream revegetation efforts and the construction of a walking and cycleway along this stream (1) (also refer to TM7.3).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	40%

Action Progress Comments: Update from Committee: The MOU is under review. No volunteer work is currently occurring.

Last Updated: 08-Dec-2022

2.14.6 Transport

Action Title: 9.1.5.188 TM7.1 Advocate with NZTA to provide a pedestrian and cycle bridge across SH21(5).

Responsible Person	Status	Start Date	End Date	% Complete
Ross Bayer - Roading Team Leader	Completed	01-Jul-2022	30-Jun-2023	100%

Action Progress Comments: North-South connectivity achieved with completion by NZTA of underpass in conjunction with Te Awa Cyclepath.

Last Updated: 08-Aug-2022

Action Title: 9.1.5.189 TM7.1a Access across SH21 at roundabout.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Ongoing	01-Jul-2022	30-Jun-2023	-0%

Action Progress Comments: Achieved though not at roundabout.

Last Updated: 08-Aug-2022

Action Title: 9.1.5.190 TM7.1b Pedestrian and cyclist access across Expressway on and off ramps at Airport interchange.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Ongoing	01-Jul-2022	30-Jun-2023	-0%

Action Progress Comments: Still to achieve any implementation of solution, but NZTA has now completed technical report with triggers for other than at-grade solutions.

Last Updated: 08-Aug-2022

Action Title: 9.1.5.191 TM7.2 Work with public transport provider to ensure the Hamilton / Cambridge bus will loop past the new retirement village (6) and commercial hub.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jun-2022	31-Dec-2024	40%

Action Progress Comments: Progress with the accessibility subsidised arrangement now in place and soon to commence WRC funded trial of extension to Hillcrest bus service being extended to Tamahere on partial basis. Also inclusion of PT for Tamahere in the new Regional Transport plan.

Last Updated: 08-Aug-2022

Action Title: 9.1.5.192 TM7.3 Support the community with the extension of shared paths (walking / cycling) through natural areas.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	40%

Action Progress Comments: MOU not complete.

Last Updated: 08-Dec-2022

Action Title: 9.1.5.193 TM8.1 Investigation of service centre, funded through LTP.

Responsible Person	Status	Start Date	End Date	% Complete
Megan May - Acting General Manager - Service Delivery	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Tamahere Service Center is now open and operating.

Last Updated: 01-Jun-2022

2.15 Taupiri

2.15.1 Communities

Action Title: 9.1.5.195 TP4.1 Redevelop the Bob Byrne Memorial Park. Consider extending it along road reserve and creating visitor activity and a local social node through the construction of a jetty (1).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: This initiative has not been progressed. If required, will need to be planned for in next LTP <i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.196 TP4.2 Facilitate boating / water recreation opportunities.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Clarification required on whether community wants more boat ramps; there is already a large one under Taupiri Mountain. <i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.197 TP4.3 Support the creation of youth activities that are cultural and community based.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: <i>Last Updated: 21-Dec-2021</i>				

2.15.2 Economy

Action Title: 9.1.5.199 TP6.1 Support when appropriate the upgrade of the local dairy to a supermarket, as the population grows.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: No progress has been made on this yet. <i>Last Updated: 17-May-2022</i>				

Action Title: 9.1.5.200 TP6.2 Develop a town centre plan to address fragmentation and services required to support employment and residential growth (2). Also consider the impact of a new service centre at the interchange and the new entrance into Taupiri from the Expressway (3).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	40%
Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones). The Ngaruawahia, Hopuhopu and Taupiri Structure Plan is currently underway and will look at all land use within the Taupiri community. <i>Last Updated: 30-May-2023</i>				

Action Title: 9.1.5.201 TP6.3 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	40%
<p>Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).</p> <p>The Ngaruawahia, Hopuhopu and Taupiri Structure Plan is currently underway and will look at all land use within the Taupiri community.</p> <p><i>Last Updated: 30-May-2023</i></p>				

Action Title: 9.1.5.202 TP6.4 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	40%
<p>Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).</p> <p>The Ngaruawahia, Hopuhopu and Taupiri Structure Plan is currently underway and will look at all land use within the Taupiri community.</p> <p><i>Last Updated: 30-May-2023</i></p>				

2.15.3 Growth

Action Title: 9.1.5.198 TP5.1 Investigate the opportunity for industrial land (refer to District-wide proposals).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2024	40%
<p>Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).</p> <p>The Ngaruawahia, Hopuhopu and Taupiri Structure Plan is currently underway and will look at all land use within the Taupiri community.</p> <p><i>Last Updated: 30-May-2023</i></p>				

2.15.4 Identity

Action Title: 9.1.5.194 TP1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Taupiri, consider Taupiri maunga, the 'village feel', and the historical sawmill and flaxmill.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
<p>Action Progress Comments: Formation of community Trust to oversee and obtain funding for community led projects.</p> <p><i>Last Updated: 31-May-2022</i></p>				

2.15.5 Infrastructure

Action Title: 9.1.5.207 TP8.1 Public toilets required at reserve.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%
<p>Action Progress Comments: District public toilet strategy being developed. A toilet is provided at Bob Bryne Reserve, the Taupiri Domain has toilets in the netball clubrooms, but are shut when netball is not being played due to vandalism issues.</p>				

Last Updated: 01-Jun-2022

2.15.6 Transport

Action Title: 9.1.5.203 TP7.1 Ensure connectivity through the proposed Lovell development to the existing street network and the proposed service centre (4).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2024	10%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

The Ngaruawahia, Hophopu and Taupiri Structure Plan is currently underway and will look at all land use within the Taupiri community and how these areas will connect to one another through roads, walking and cycling.

Last Updated: 30-May-2023

Action Title: 9.1.5.204 TP7.2 Investigate the possibility of constructing a bridge across the Waikato River to connect east and west.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: No progress has been done to date on this. The cost to pursue a piece of infrastructure of this scale is very high. There would need to be a business case that demonstrates the benefits of connecting the East and West of the Waikato River. In Taupiri a trust has been set up to pursue a walkway network which is supported by the community.

Last Updated: 31-May-2023

Action Title: 9.1.5.205 TP7.3 Allow for the continuation of the Te Awa cycle trail (refer to District-wide proposals).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments:

Last Updated: 21-Dec-2021

Action Title: 9.1.5.206 TP7.4 Consider cycling and walking to and from the school as the town expands.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments: to be developed as part of the next LTP, programme for this ltp is full

Last Updated: 02-Jun-2022

2.16 Tuakau

2.16.1 Communities

Action Title: 9.1.5.2 TU4.1 Support the local initiative to establish a community hub, which may be partially privately funded.

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: OTCB applied for building consent to expand the existing youth center. This consent was paid for by WDC but no progress was made on behalf of the community. WDC staff will continue to support this initiative.

Last Updated: 12-May-2023

Action Title: 9.1.5.3 TU4.3 Develop a sports and recreation facility, including consideration of incorporation of the Council's pool facility.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	10%

Action Progress Comments: Work has been completed through Sport Waikato to support the Dr John Lightbody Sports Society to utilise the existing sports pavillion building. Additional renewal work is due to occur at the Tuakau Pools to improve that asset.

Last Updated: 30-May-2023

Action Title: 9.1.5.4 TU4.4 Support and enhance library services.

Responsible Person	Status	Start Date	End Date	% Complete
Brian Cathro - Customer Support Projects Manager (secondment)	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Complete. Refurb and extension of Tuakau library was completed in 2021.

Last Updated: 31-May-2022

Action Title: 9.1.5.9 TU4.2 Support the community aspirations for an emergency services hub.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Lease has been provided for Lightbody Reserve building to use as community/emergency hub.

Last Updated: 02-Jun-2023

Action Title: 9.1.5.20 TU4.5 Install lighting and CCTV for safety.

Responsible Person	Status	Start Date	End Date	% Complete
Megan May - Acting General Manager - Service Delivery	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: CCTV cameras are already installed in Tuakau and a recent upgrade to the server has future proofed this.

Last Updated: 01-Jun-2022

2.16.2 Economy

Action Title: 9.1.5.6 TU6.7 Prepare a strategy for the promotion of Tuakau for living and visiting.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments:				
<i>Last Updated: 18-Nov-2021</i>				

Action Title: 9.1.5.12 TU6.1 Prepare a town centre strategy considering character, provision of green spaces, streetscape upgrades, mix of uses, anchors etc. (2).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2023	30-Jun-2025	0%
Action Progress Comments: Other town centres (Pokeno & Ngaruawahia) have taken priority to date. Council will determine the priority list of where to next for Town Centre Planning as part of the 2024-2034 Long Term Plan.				
<i>Last Updated: 01-May-2023</i>				

Action Title: 9.1.5.13 TU6.6 Ensure that the timing of job creation aligns with residential growth.

Responsible Person	Status	Start Date	End Date	% Complete
Emma Rankin - Economic Development and Key Account Manager	Ongoing	01-Jul-2021	30-Jun-2024	-0%
Action Progress Comments: The zoning for employment in Tuakau has been in place for many years. The Proposed District Plan Decision has allowed for additional residential zoning. Council cannot determine the timing of jobs to the market. Staff could assist business owners but this is community led.				
<i>Last Updated: 16-May-2022</i>				

Action Title: 9.1.5.14 TU6.8 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%
Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).				
<i>Last Updated: 01-May-2023</i>				

Action Title: 9.1.5.15 TU6.9 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%
Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).				
<i>Last Updated: 01-May-2023</i>				

Action Title: 9.1.5.16 TU6.2 Consider employment uses south of town centre along River Road (see strategic diagram) (3).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2024	100%

Action Progress Comments: This area was considered for additional development as part of the Structure Plan, the Proposed Waikato District Plan and Waikato 2070 (Councils Growth and Economic Development Strategy). Other areas for development were identified in fitting with creating compact urban environments. Since these plans were developed the National Policy Statement on Highly Productive Land has been released. This is to protect Highly Productive Land for primary productivity from development and would apply to this area.

Last Updated: 30-May-2023

Action Title: 9.1.5.17 TU6.3 Establish a Designers and Makers Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 01-Jun-2022

Action Title: 9.1.5.18 TU6.4 Establish a Designer Food Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 01-Jun-2022

Action Title: 9.1.5.19 TU6.5 Investigate opportunities for short-stay courses.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 18-Nov-2021

2.16.3 Growth

Action Title: 9.1.5.10 TU5.1 Consider areas for expansion, reconciling possible growth demand with high class soils and contours.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The Decision on the Proposed District Plan identifies areas for future residential expansion while considering contours and high class soils. This saw some zoning in the west reconciled back to rural.

Last Updated: 16-May-2022

Action Title: 9.1.5.11 TU5.2 Address the interface between residential and industrial land. Consider sports fields as a buffer (1).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Careful consideration by the hearings panel was given to the location of Residential sites in relation to Industrial sites. Stronger Policies have been put in place to help mitigate effects of industry near sensitive land uses.

Last Updated: 16-May-2022

2.16.4 Identity

Action Title: 9.1.5.1 TU1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area,

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not started				
<i>Last Updated: 10-May-2022</i>				

2.16.5 Infrastructure

Action Title: 9.1.5.5 TU8.1 Build public toilets.

Responsible Person	Status	Start Date	End Date	% Complete
Megan May - Acting General Manager - Service Delivery	Completed	01-Jul-2021	30-Jun-2022	100%
Action Progress Comments: The new toilets at St Stephens Ave have now been completed and are open. Based on community feedback in July 2022, more toilets are desired but no specific details of where are provided.				
<i>Last Updated: 26-May-2022</i>				

2.16.6 Transport

Action Title: 9.1.5.7 TU7.1 Provide advocacy for the widening of existing, and / or the construction of new, road connections to SH1.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Ongoing	01-Jul-2024	30-Jun-2026	-0%
Action Progress Comments: this project is not included in this LTP				
<i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.8 TU7.2 Create a Park and Ride for public transport (for consideration 2024-2034 LTP)

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: The Pookeno-Tuakau-Pukekohe bus service was launched in January 2021. It has provided a reliable and safe public transport option connecting these towns (and importantly, connecting Pokeno and Tuakau to the Pukekohe station park and ride within the Auckland boundary). However the Pukekohe Railway Station has been closed from 13 August 2022 as KiwiRail is redeveloping the station and the rail line to allow for Auckland Transport's electric trains to travel between Pukekohe and Papakura. The Pukekohe train service has been suspended until late 2024. Bus route 394 is a free replacement bus between Papakura and Pukekohe via Paerata Rise. Customers can transfer at Papakura Station for travel on the Southern Line to other destinations.				

The short and long term benefits of where the next railway station in the Waikato district should be located is being considered through the Upper Northern Waikato Railway Station Indicative Business Case (due for completion by end June 2023). There is no funding to progress a park and ride facility as part of any station (let alone the construction of a platform for any either Tuakau, Pookeno or Te Kauwhata in the current LTP). Council does however own land adjacent where the potential railway platform should be in Pookeno and Te Kauwhata so this is an advantage. Consideration for land acquisition to future proof a potential station and/or park and ride facility at Tuakau will need to happen through the 2024 LTP together with consideration of a future station in the northern Waikato (whether it be Te Kauwhata, Pokeno or Tuakau). The indicative business case will inform where this station should be.

Last Updated: 19-Apr-2023

2.17 Whatawhata

2.17.1 Communities

Action Title: 9.1.5.210 WW4.1 Support the process to create a meeting space ('Our Place').

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	In Progress	01-Jul-2021	30-Jun-2024	30%

Action Progress Comments: Blueprint funding allocated to this project. Wellbeing Trust funding and Rural Ward Funding allocated also.

Last Updated: 31-May-2023

Action Title: 9.1.5.211 WW4.2 Facilitate an investigation into the options for expanding the School. Consider expansion towards the east (1).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: This needs to be led by the Ministry of Education.

Last Updated: 17-May-2022

Action Title: 9.1.5.212 WW4.3 Create public picnic areas with BBQ facilities.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: There is insufficient Council land in Whatawhata except for the Whatawhata Recreation Reserve as majority of land bounds highways, and exiting and entering is a safety concern.

Last Updated: 01-Jun-2022

2.17.2 Economy

Action Title: 9.1.5.213 WW6.1 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	5%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

Action Title: 9.1.5.214 WW6.2 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	5%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

2.17.3 Identity

Action Title: 9.1.5.208 WW1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Whatawhata, consider the village as a service centre for the rural periphery and local marae.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: <i>Last Updated: 21-Dec-2021</i>				

2.17.4 Infrastructure

Action Title: 9.1.5.219 WW8.1 Consider constructing new facilities as part of the proposed sports fields expansion (WW4.3).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	10%
Action Progress Comments: Unfortunately, the Whatawhata Rugby club burnt down and have left the Whatawhata Domain with no facility. Community Connections team and Sport Waikato are working with the Whatawhata Rugby Committee to support the rebuild of their club building and ensure what ever is built suits the needs of the community. <i>Last Updated: 01-Jun-2022</i>				

2.17.5 Nature

Action Title: 9.1.5.209 WW2.1 Address river bank weeds and erosion issues.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Ongoing liaison with WRC and roading alliance on issues as resources allow. <i>Last Updated: 01-Jun-2022</i>				

2.17.6 Transport

Action Title: 9.1.5.215 WW7.1 Support NZTA discussions to deliver the roundabout to resolve congestion and safety concerns (2).

Responsible Person	Status	Start Date	End Date	% Complete
Gareth Bellamy - Senior Transportation Engineer	Completed	01-Jul-2021	30-Jun-2022	100%
Action Progress Comments: this is an nzta project and not responsibility of council. design is underway by waka kotahi, no dates for construction <i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.216 WW7.2 Extend local footpaths to connect new residential areas to the village centre.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: outside this LTP as programme is full <i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.217 WW7.3 Investigate reinstating the Makarini Road bridge across the Waipa to improve connectivity between the village centre and residential expansion areas to the west.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: this project is unlikely to go ahead as there is already crossing facilities, will consider if west side of the waipa river intensifies as its not in the PDP <i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.218 WW7.4 Create public river access to the west of the village centre.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Budget was allocated through last LTP to install a boat ramp. Community decision was made to reallocate funding to playground and then reallocated to the Community Facility build.

Last Updated: 01-Jun-2022

2.18 District Wide

2.18.1 Communities

Action Title: 9.1.5.237 DW4.1 Continue the implementation of the strategy for the upgrade of sporting facilities and reserves.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: Staff continue to consider land acquisition opportunities for areas of the district which are under provisioned in sports fields.

Last Updated: 01-Jun-2022

Action Title: 9.1.5.238 DW4.10 Determine a strategy for the clean-up of building frontages and streetscape in town centres and other key areas.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Jan-2022

Action Title: 9.1.5.239 DW4.11 Improve accessibility of the Council's website and social media.

Responsible Person	Status	Start Date	End Date	% Complete
Emma Edgar - Executive Manager - Communications & Engagement	In Progress	01-Jul-2021	30-Jun-2024	42%

Action Progress Comments: We are in the process of refreshing our social media strategy to ensure that it is up to date and most fit for purpose taking into consideration new approaches and platforms to reach our communities. We will be implementing this soon but in the interim have started increasing our reach through existing channels with enhanced content and campaigns/ messaging that resonate. We will soon be looking at our website refresh and how to ensure that we are leveraging this platform to best effect.

Last Updated: 31-May-2022

Action Title: 9.1.5.240 DW4.12 Determine a strategy for facilitating local communities in their communications (website / social media).

Responsible Person	Status	Start Date	End Date	% Complete
Emma Edgar - Executive Manager - Communications & Engagement	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Feel this is a duplication of this first objective - can it be removed or this one be kept and the other removed? Progress update on this above.

Last Updated: 15-Jul-2022

Action Title: 9.1.5.241 DW4.13 Support events organised by local communities.

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: Events team has been created within Council. The team is currently working on community-led events to ensure compliance with strategies, health & safety, traffic management. Plans in place to create an

Last Updated: 12-May-2023

Action Title: 9.1.5.242 DW4.2 Complete a strategy for the upgrade of arts facilities.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Jan-2022

Action Title: 9.1.5.243 DW4.3 Resolve access needs to Hamilton libraries.

Responsible Person	Status	Start Date	End Date	% Complete
Brian Cathro - Customer Support Projects Manager (secondment)	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Complete. We signed a new contract in 2019 for residents that boarder HCC boundaries.

Last Updated: 31-May-2022

Action Title: 9.1.5.244 DW4.4 Address lack in medical services and isolation issues.Address lack in medical services and isolation issues.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Jan-2022

Action Title: 9.1.5.245 DW4.5 Implement the public toilet strategy.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: Implementing as per works programme. Strategy to be reviewed to consider the expectation of customers and communities while considering budget restraints.

Last Updated: 01-Jun-2022

Action Title: 9.1.5.246 DW4.6 Implement the youth strategy.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

Action Title: 9.1.5.247 DW4.7 Determine a strategy for addressing the lack in aged care facilities.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Jan-2022

Action Title: 9.1.5.248 DW4.8 Undertake a social audit to determine which services are being funded and by whom, which gaps exist, and whether there is any duplication.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Jan-2022

Action Title: 9.1.5.249 DW4.9 Support safer communities initiatives.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 14-Jan-2022

2.18.10 Other

Action Title: 9.1.5.281 DW10.1 Civic pride via higher levels of service to less well-served areas of town, and targeting spots around town that bring the feel of the place down for clean up.

Responsible Person	Status	Start Date	End Date	% Complete
Trisha Morrison - Community Assets Manager	In Progress	01-Jul-2021	30-Jun-2024	25%

Action Progress Comments: 12/5/23 - Levels of Service are being considered as part of Asset Management Planning and Activity Management Planning for the 2024-2034 Long Term Plan

Last Updated: 12-May-2023

2.18.2 Economy

Action Title: 9.1.5.254 DW6.1 Determine additional industrial, commercial and retail land needs.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

Action Title: 9.1.5.255 DW6.2 Determine if, how much, and where possible future employment (land for office development) zoning opportunities beyond the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

Action Title: 9.1.5.256 DW6.3 Determine if, how much, and where possible future retail zoning opportunities beyond the Proposed District Plan lie.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

Action Title: 9.1.5.257 DW6.4 Investigate the industrial land opportunities as identified in the Blueprint project.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

Action Title: 9.1.5.258 DW6.5 Investigate the clean production land opportunities as identified in the Blueprint project.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 17-Jan-2022

Action Title: 9.1.5.259 DW6.6 Determine a youth into employment strategy, possibly in conjunction with existing entities in this space.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 17-Jan-2022

Action Title: 9.1.5.260 DW6.7 Develop a visitor attraction strategy preferably focussed on 1.5-hour attractions.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 17-Jan-2022

2.18.3 Governance

Action Title: 9.1.5.277 DW9.1 Support non-Council external entities in their endeavours where their objectives align with the Council's objectives.

Responsible Person	Status	Start Date	End Date	% Complete
Nick Johnston - Advocacy and Investment Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 17-Jan-2022

Action Title: 9.1.5.278 DW9.2 Determine ways of better utilising Geographic Information System (GIS) services.

Responsible Person	Status	Start Date	End Date	% Complete
Anton Marais - Business Intelligence Team Leader	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: No actions initiated, no planning for how Blue Print mapping and visualization of Blue prints has been investigated

Last Updated: 08-Jun-2022

Action Title: 9.1.5.279 DW9.3 Give the Blueprint status.

Responsible Person	Status	Start Date	End Date	% Complete
Jim Ebenhoh - Planning and Policy Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The Blueprint has informed the 2021 LTP and continues to be a touchstone for planning, operations, service delivery, etc. This quarterly reporting exercise is another example of the Blueprint being given status.

Last Updated: 17-May-2022

Action Title: 9.1.5.280 DW9.4 Enable the devolution of the management of limited projects to local committees, justified by a business case. First undertake a 'local provision' scoping study.

Responsible Person	Status	Start Date	End Date	% Complete
Jim Ebenhoh - Planning and Policy Manager	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: This is a complicated initiative involving (potentially) co-design as well as empowering communities to deliver projects - but with health and safety considerations etc. The Economic and Community Led Development team's recent work with communities on their Blueprint and other priorities is an example of this being work in progress. Progress updates on other Blueprint initiatives demonstrate what has been achieved.

Last Updated: 25-May-2023

2.18.4 Growth

Action Title: 9.1.5.250 DW5.1 Review the District Development (Growth) Strategy based on revised population and household projections.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The District Development Strategy was reviewed in 2019 and adopted by Council 2020. The review saw the Economic Development Strategy and Development Strategy combined. The Waikato District

Last Updated: 31-May-2022

Action Title: 9.1.5.251 DW5.2 Assess the plan enabled and commercially feasible residential, business and industrial capacity against the new projections, followed by an exercise to determine future residential, business and industrial zoning opportunities beyond the PDP.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2024	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 31-May-2023

Action Title: 9.1.5.252 DW5.3 Undertake preparatory work in advance of an affordable housing strategy.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2022	20%

Action Progress Comments: Council workshops have been held regarding affordability and data is being monitored.

Last Updated: 17-May-2022

Action Title: 9.1.5.253 DW5.4 Implement design guidance.

Responsible Person	Status	Start Date	End Date	% Complete
Keri Davis-Miller - Resource Management Policy Manager	Not Started	01-Jul-2021	30-Jun-2022	0%
Action Progress Comments: The Proposed District Plan Decision removed to urban design guidance. Work needs to be completed to understand next steps with regards to urban design guidance.				
<i>Last Updated: 17-May-2022</i>				

2.18.5 Identity

Action Title: 9.1.5.220 DW1.1 Build a strong river corridor identity.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments:				
<i>Last Updated: 10-Jan-2022</i>				

Action Title: 9.1.5.221 DW1.2 Build the identity of each town under the umbrella of the entire District.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments:				
<i>Last Updated: 13-Jan-2022</i>				

Action Title: 9.1.5.222 DW1.3 Promote cultural tourism in the river corridor.

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments:				
<i>Last Updated: 13-Jan-2022</i>				

2.18.6 Infrastructure

Action Title: 9.1.5.266 DW8.1 Progress the contract arrangement with Watercare for the delivery of water operations within the district.

Responsible Person	Status	Start Date	End Date	% Complete
Carole Nutt - Waters Contract Relationship Manager	Completed	01-Jul-2021	30-Jun-2024	100%
Action Progress Comments: Developed delineation table and graphics as part of the Stormwater Collaboration Workshops to demarcate ownership and maintenance responsibility of assets between WDC (Roading, Open Spaces), WSL, WRC and other entities. Delineation Graphics are also available on website for public use and information. Rural drainage asset base with WRC for stormwater.				
<i>Last Updated: 27-Apr-2022</i>				

Action Title: 9.1.5.267 DW8.10 Central Waikato

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Jun-2026	2%

Action Progress Comments: Nga WWTP non-compliant with discharge consent during 2020-21 period, current operations include; desludging of the pond, O&M plan to be submitted May 2022. Planning underway to address current non-compliances by July 2023 date. Nga WWTP upgrade is an option in the Northern Metro WW DBC. Considering bringing Huntly upgrades forward in light of development in Ohenewai. This is being undertaken as part of BAU.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.268 DW8.11 Southern Waikato and Small Schemes

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	In Progress	01-Jul-2021	30-Jun-2024	99%

Action Progress Comments: The existing Horotiu zoning is serviced or will be serviced for water and wastewater in the 2021-2031 LTP. Consideration of new zoning, and consideration of servicing Te Kowhai will be considered in the preparation of the next LTP.

The exploration of cross boundary solutions has been considered through the Northern Hamilton-Waikato Metropolitan Wastewater Detailed Business Case. The DBC has been adopted and has recommended a long term servicing solution which entails taking wastewater from Ngaaruwaahia, Taupiri, Hopuhopu, Te Kowhai and Horotiu to a future-upgraded Pukete Wastewater Treatment Plant post 2041. Any future planning for this work will need to be undertaken by the new water entity.

Last Updated: 24-Apr-2023

Action Title: 9.1.5.269 DW8.2 North Waikato

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Jun-2023	10%

Action Progress Comments: This is being undertaken as part of BAU and shortfall needs to be addressed before physical works can commence.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.270 DW8.3 Raglan - Raglan wastewater upgrade.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Jun-2026	10%

Action Progress Comments: This is being undertaken as part of BAU, refer to the Waters Governance Report meeting for updates and the upgrade is being considered as part of the consent renewal.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.271 DW8.4 Mid Waikato - Te Kauwhata wastewater treatment plant (WWTP) (short and long term).

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	01-Jan-2023	40%

Action Progress Comments: A capital solution for the Te Kauwhata WWTP is currently in design to address the abatement notice and significant works are underway. This is being undertaken as part of BAU and reported in the open section of the Waters Governance Board meeting.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.272 DW8.5 Central Waikato

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Sep-2024	70%

Action Progress Comments: Refer to Waters Governance Board (open section of the meeting) for detail.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.273 DW8.6 North Waikato - Pokeno and Tuakau water main upgrades.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Jun-2025	25%

Action Progress Comments: This project is underway, this year's stage is Dominion Road, Tuakau, which is nearing completion (approximately mid-May).

Last Updated: 28-Apr-2022

Action Title: 9.1.5.274 DW8.7 Mid Waikato - Te Kauwhata water-take consent renewal.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	01-Dec-2023	20%

Action Progress Comments: Continuing to work with the TKWA to ensure the allocation requested will meet Council's growth aspirations and ensure timely application for the renewal of the water take resource consent by TKWA. This is being undertaken as part of BAU and being reported at the regular Waters Governance Board meetings.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.275 DW8.8 Southern Waikato and Small Schemes

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Jun-2023	15%

Action Progress Comments: Currently considering options for Te Akau Water Supply. Te Akau Options Assessment report was taken to the WGB in March to present the preferred future water supply option to enable a final solution to be authorised. Onewhero and Port Waikato high level options will be presented to Waters Governance Board early June. Struggling to secure land for Southern Schemes water supply scheme.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.276 DW8.9 Raglan - Raglan WWTP Renewal.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	30-Jun-2023	60%

Action Progress Comments: Considering options for land-based discharge solutions that will meet the needs of Tangata whenua and the majority of the Whaingaroa Community. Private land investigations are occurring along with the possible use of Wainui reserve. Being reported at the regular community update meetings and Waters Governance Board meeting.

Last Updated: 27-Apr-2022

2.18.7 Iwi

Action Title: 9.1.5.233 DW3.1 Use the Joint Management Agreements (JMA) more effectively.

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	Completed	01-Jul-2021	30-Jun-2024	100%

Action Progress Comments: A Strategic Work Programme for 2022-2023 for the Waikato-Tainui | Waikato District Council JMA Committee was developed collaboratively and approved by JMAC on 10 August 2022. A progress update on the implementation of the 2022-2023 Strategic Work Programme was provided at the first JMAC hui of this new triennium on 14 April 2023. It was agreed at the hui that staff must develop a similar Strategic Work Programme for the 2023-2024 financial year and that some of the initiatives/projects identified in the 2022-2023 programme will logically carry over. The Strategic Work Programme is providing a more effective tool for both the tribe and Council to implement and engage on matters of mutual strategic significance.

Last Updated: 19-Apr-2023

Action Title: 9.1.5.234 DW3.2 Formulate a strategy to build engagement relationships with Hapuu and to build awareness of Council processes and practices within Hapuu.

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Jan-2022

Action Title: 9.1.5.235 DW3.3 Formulate a strategy for increasing the use of Te Reo.

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Jan-2022

Action Title: 9.1.5.236 DW3.4 Create new staff positions related to Maori partnership.

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Jan-2022

2.18.8 Nature

Action Title: 9.1.5.223 DW2.1 As a review of Waikato District Council's Conservation Strategy, investigate the development and implementation of a Local Indigenous Biodiversity Strategy for the District, jointly with Waikato Regional

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2024	90%

Action Progress Comments: The draft Taiao (Nature) in the Waikato Strategy hearings and deliberations has concluded. The strategy is with the designer and is going to the June Sustainability and Wellbeing Committee and will recommend to full Council for adoption.

Last Updated: 31-May-2023

Action Title: 9.1.5.224 DW2.10 Ensure developers know rural drainage WRC requirements up front.

Responsible Person	Status	Start Date	End Date	% Complete
Ana Maria d'Aubert - Consents Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: All developers are advised to check with Waikato Regional Council rural drainage requirements and to address relevant matters that might be applicable to a proposal.

Last Updated: 16-May-2022

Action Title: 9.1.5.225 DW2.2 Review solid waste services.

Responsible Person	Status	Start Date	End Date	% Complete
Phillip Ellis - Solid Waste Team Leader	In Progress	01-Jul-2021	31-Jul-2023	30%

Action Progress Comments: Future strategy and plan being reset with Steering Group, including aligning with clearer national direction from MFE. Pathway to implementation includes DW waste assessment and new WMMP (objectives for service and what it will become, including actions) circa July 2023; and ultimately procurement planning for new contracts at end of current contract terms.

Last Updated: 25-May-2022

Action Title: 9.1.5.226 DW2.3 Complete the ongoing data capture and condition assessment of storm water assets.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	In Progress	01-Jul-2021	01-Jul-2025	20%

Action Progress Comments: WDC and now Watercare are capturing Stormwater data on a catchment per year basis. It is expected this will take until 2025 to complete.

Last Updated: 27-Apr-2022

Action Title: 9.1.5.227 DW2.4 Build a greater awareness of the Waikato Regional Council (WRC) storm water guidelines across WDC.

Responsible Person	Status	Start Date	End Date	% Complete
Ana Maria d'Aubert - Consents Manager	In Progress	01-Jul-2021	30-Jun-2024	90%

Action Progress Comments: The Waikato Regional Council has two Technical Reports relating to stormwater accessible on its website: "Waikato Stormwater Management Guideline (TR2020/70)" and "Waikato Stormwater Runoff Modelling Guideline (TR2020/16)".

The Waikato District Council (Waters team) is developing its own "Waikato District Council Stormwater Design Guidelines, REV 9" which are scheduled to be finalized late May 2022. The Waikato District guidelines will make reference to the Waikato Regional guidelines, and when finalized they will be available on Waikato District Councils website.

Together all these guidelines will ensure developers and applicants for resource consent are aware of stormwater requirements for subdivisions and development.

This Actin is to be reassigned to the Waters team.

Last Updated: 17-May-2022

Action Title: 9.1.5.228 DW2.5 Drive Low Impact Urban Design (LIUD) approaches through Catchment Management Plans and Integrated Catchment Management Plans.

Responsible Person	Status	Start Date	End Date	% Complete
Ana Maria d'Aubert - Consents Manager	In Progress	01-Jul-2021	30-Jun-2024	90%

Action Progress Comments: The Waikato District Council does from time to time prepare catchment management plans. As and when they are reviewed or new ones prepared, they will encourage Low Impact Urban Design (LIUD) approaches. However, developers do not need to rely only on these plans in order to implement them.

LIUD approaches will be part of the "Waikato District Council Stormwater Design Guidelines, REV 9" which are scheduled to be finalized late May 2022 (and then available on the website). In addition, the Waikato Regional Council has two Technical Reports relating to stormwater accessible on its website that also encourage LIUD: "Waikato Stormwater Management Guideline (TR2020/70)" and "Waikato Stormwater Runoff Modelling Guideline (TR2020/16)".

Together all these guidelines encourage LIUD approaches in development where appropriate.

This Action is to be reassigned to the Waters team.

Last Updated: 17-May-2022

Action Title: 9.1.5.229 DW2.6 Lead by example by applying low impact storm water approaches in Council works.

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	Ongoing	01-Jul-2021	30-Jun-2023	-0%

Action Progress Comments: Initiative from Stormwater team (this initiative/action involves other entities as well as developers/public): Currently finalising WDC Stormwater Guidelines document to provide some guidance in terms of good design practices and preference to achieve multiple benefits from land development.

Last Updated: 21-Apr-2022

Action Title: 9.1.5.230 DW2.7 Investigate options to promote LIUD, e.g. through a remission of Development Contributions or an eco-design advice service.

Responsible Person	Status	Start Date	End Date	% Complete
Will Gauntlett - Growth and Analytics Manager	In Progress	01-Jul-2021	30-Jun-2023	5%

Action Progress Comments: The first leg of this action will be considered as part of the next DC Policy Review. It has been added to an issues and options document. The second leg of this action needs to be split off and reassigned to another team.

Last Updated: 18-Apr-2023

Action Title: 9.1.5.231 DW2.8 Develop a better understanding of the rural drainage asset base and roles and responsibilities (WDC and WRC).

Responsible Person	Status	Start Date	End Date	% Complete
Carole Nutt - Waters Contract Relationship Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Developed delineation table and graphics as part of the Stormwater Collaboration Workshops to demarcate ownership and maintenance responsibility of assets between WDC (Roading, Open Spaces), WSL, WRC and other entities. Delineation Graphics are also available on website for public use and information.

Last Updated: 21-Apr-2022

Action Title: 9.1.5.232 DW2.9 Confirm the Council's approach to drainage, and ensure it is reflected in the consenting process.

Responsible Person	Status	Start Date	End Date	% Complete
Ana Maria d'Aubert - Consents Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Where land drainage is relevant to a proposal, applicants are required to assess effects, level of risk to development, and propose methods and mitigation measures if necessary, prior to consent being granted.

Approaches to land drainage may be relevant at both a Waikato Regional Council and/or a Waikato District Council level.

The Waikato Regional Council has two Technical Reports relating to stormwater accessible on its website: "Waikato Stormwater Management Guideline (TR2020/70)" and "Waikato Stormwater Runoff Modelling Guideline (TR2020/16)".

The Waikato District Council (Waters team) is developing its own "Waikato District Council Stormwater Design Guidelines, REV 9" which are scheduled to be finalized late May 2022. The Waikato District guidelines will make reference to the Waikato Regional guidelines, and when finalized they will be available on Waikato District Councils website.

Together all these guidelines will ensure developers and applicants for resource consent are aware of land drainage and stormwater requirements for subdivisions and development.

Last Updated: 16-May-2022

2.18.9 Transport

Action Title: 9.1.5.261 DW7.1 Refer to Identity for cycling and walking tracks.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments:				
<i>Last Updated: 17-Jan-2022</i>				

Action Title: 9.1.5.262 DW7.2 Secure an improved bus service for the entire Waikato District.

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	In Progress	01-Jul-2021	30-Jun-2024	35%

Last Updated: 19-Apr-2023

Action Title: 9.1.5.263 DW7.3 Support the Waikato train stations within the Auckland to Hamilton Corridor project.

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Action Progress Comments: New bus services have been considered in the current (2021-2031) LTP for the Raglan (internal), Pokeno (to Papakura), Tamahere, Matangi and Te Kowhai communities (the latter three all connecting to Hamilton). Council approved funding in the 2021-2031 LTP for these services and submitted via Waikato Regional Council for Waka Kotahi funding. Due to national budget constraints and low national bus service patronage, the proposed services did not attract Waka Kotahi subsidy. Waikato District Council and Waikato Regional Council staff have reviewed the local share funding and propose to utilise the local share to wholly fund the Raglan, Tamahere, Matangi and Pokeno services as “trial services” in the first instance.

Unfortunately, the shortage of bus drivers in 2022 and the first half of 2023 has meant that the Regional Council has not been able to progress operationalising these services. The priority services have been identified as the Raglan internal service, the proposed Pokeno to Papakura service and the proposed Matangi-Tamahere-Hamilton service. The fee proposal for the Raglan internal service has been signed by the Regional Council and service implementation is underway.

Waikato Regional Council and Waikato District Council staff will be holding a workshop with the Tamahere Community Committee and the Matangi Community Committee on 2 May 2023 to discuss the proposed Matangi-Tamahere-Hamilton service. An online workshop is also planned for end May 2023 to discuss the proposed Pokeno to Papakura Railway Station service (and its potential implication for the existing Pokeno-Tuakau-Pukekohe service).

These will remain trial services until Waka Kotahi subsidy is obtained and the existing funding is exhausted. Council will be advocating for the subsidy and considering its own contribution for these services in its 2024-2034 LTP. Patronage uptake will be a key determinant as to whether these trials will continue or not.

Action Progress Comments: Council has now acquired the adjacent Go Bus land at the Raahui Pookeka | Huntly Railway Station for expanding the current park and ride facility. The land is being leased to Go Bus in the interim until the company has secured another site in Huntly/Ohinewai for its buses. Council will then need to undertake remedial works on the newly-acquired site to ensure that bus thoroughfare can be accommodated so that passengers can be picked up or disembark at the Raahui Pookeka | Huntly Railway Station.

The relocation of the historic Huntly Railway Station building to the Raahui Pookeka Railway Station is imminent (by end April 2023). The building will house the Huntly Waikato Coalfields Museum as well as provide an ablution facility for passengers.

With regards to potential railway stations in other towns (especially Te Kauwhata, Pokeno and Tuakau) there is currently no funding in the LTP for land acquisition and/or station construction. The development of a second passenger railway station in the district is subject to government funding and partnership support. Council (together with the Waikato Regional Council and Waka Kotahi) have however commenced the development of an indicative business case (feasibility study) for a railway station in the northern Waikato. This work is expected to be completed at the end of June 2023.

A detailed business case (for which there is no committed funding) will then have to be done for a potential station. Funding for the detailed business case will be a matter for consideration in the 2024-2034 LTP. Should there be further park and ride facilities created in the future, these would be constructed to cater for both cars and buses.

Last Updated: 19-Apr-2023

Action Title: 9.1.5.264 DW7.4 Continue to monitor the consequences of State Highway projects on the Waikato District and its local communities, and when possible fulfil an advocacy role to positively influence outcomes.

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	In Progress	01-Jul-2021	30-Jun-2024	80%

Action Progress Comments: By all intents and purposes communities and road users have settled in well and accepted the new road configurations enabled by the Waikato Expressway. Whilst the reduced traffic flow through Huntly and Ngaruawahia has improved safety, it has meant a reduced customer base for the local businesses (due to reduced through-traffic). However, these towns continue to grow as far as their population is concerned so this will be of benefit to local businesses. A structure plan is currently being developed for Ngaaruawaahia | Hopuhopu | Taupiri to accommodate long term growth.

The Expressway has improved safety and efficiency to Auckland and further south into the Waikato.

The main focus for Council staff at present (and in so far as access to the Expressway is concerned) relates to the Meremere A industrial area to east of the Waikato Expressway. The strategic issue at Meremere for Tainui Group Holdings (who administer the land on behalf of the tribe) is eventually unlocking the development of Meremere A for a major recycling centre of excellence (notwithstanding the infrastructure challenges). This is the long-term outcome that TGH aspires to.

TGH and WDC have held joint meetings with Waka Kotahi to explore options for the short term and long-term access to the Waikato Expressway from Meremere A. Waka Kotahi has advised TGH that resource consent will be required as a restricted discretionary activity under Rule TRPT-R4 (Traffic Generation) of the Proposed Waikato District Plan- Decisions Version, due to the number of heavy vehicles proposed for access in and out of the site. There are currently safety challenges at the Island Block Road/Waikato Expressway intersection. Specifically, in relation to HCV's using the left turn slip lane into Island Block Road as this will obscure visibility to those trying to exit Island Block Road.

Waka Kotahi wants to understand the adverse effects on the Island Block Road/Waikato Expressway intersection because of the additional heavy vehicle movements. This would best be done in the form of an Integrated Transport Assessment (ITA). Once a traffic engineer has been engaged by TGH, Waka Kotahi will organise a meeting prior to an ITA being undertaken to discuss the scope/methodology of the ITA contents.

Last Updated: 19-Apr-2023

Action Title: 9.1.5.265 DW7.5 Strengthen cycling and walking trails along the river corridor.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: Additional stages of Te Awa cycle trail now completed and open.

Last Updated: 01-Jun-2022

2.2 Horotiu

2.2.1 Economy

Action Title: 9.1.5.24 HO6.3 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	5%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 01-May-2023

Action Title: 9.1.5.25 HO6.1 Establish an Advanced Food Processing Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 23-Nov-2021

Action Title: 9.1.5.26 HO6.2 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 01-May-2023

2.2.2 Growth

Action Title: 9.1.5.27 HO5.2 Investigate the opportunity for additional industrial land (also refer to District-wide proposals) (2).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Waikato 2070 does identify where to next with Industrial land in Horotiu and this will be considered as part of the assessment.

Last Updated: 01-May-2023

Action Title: 9.1.5.28 HO5.1 Explore the potential for leisure, accommodation, and residential development between SH1 and the Waikato River (1).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The Proposed District Plan Decisions and Hamilton City Council Plan Change 2 identifies Residential and Leisure activities in Horotiu between Great South Road (former SH1) and the Waikato River. Both local authorities now have operative zoning.

Last Updated: 16-May-2022

2.2.3 Identity

Action Title: 9.1.5.29 HO1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Horotiu, consider the historic Maaori gardens and the business park.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

2.2.4 Infrastructure

Action Title: 9.1.5.30 HO8.1 Fill in or improve the appearance of the open stormwater drains at the original AFFCO village in Park Road (7).

Responsible Person	Status	Start Date	End Date	% Complete
Keith Martin - Contractor - Waters Manager	Not Started	01-Jul-2021	01-Jul-2025	0%

Action Progress Comments: More information required, if this is a 'nice to have' and stormwater is operating as it should. This may not be prioritised and could be considered in the next LTP period depending on funding availability.

Last Updated: 27-Apr-2022

2.2.5 Transport

Action Title: 9.1.5.31 HO7.1 Form the paper road at the end of Sullivan Road and form a carpark to improve accessibility to the river (3).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments:

Last Updated: 23-Nov-2021

Action Title: 9.1.5.32 HO7.2 Provide longer distance walking and cycling connections to Te Kowhai and Horsham Downs (4) (refer to DW1.3).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments: to be considered in the next LTP Considerations, the 2021/24 programme is full

Last Updated: 02-Jun-2022

Action Title: 9.1.5.33 HO7.3 Provide a walking and cycling route on the eastern side of the Waikato River between Horotiu and Ngaruawahia to create a loop with the Te Awa river ride (5) (also refer to DW1.3).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Deferred	01-Jul-2024	31-Mar-2026	1%

Action Progress Comments: unlikely to progress as does not align with trails strategy

Last Updated: 01-Jun-2022

Action Title: 9.1.5.34 HO7.4 Investigate safety improvements and traffic calming along River Road as well as connections to the proposed route along the eastern side of the river (HO73) to create a loop for recreational cycling (6).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Deferred	01-Jul-2024	30-Jun-2026	1%
Action Progress Comments: refer to 9.1.5.33 HO7.3, unlikely to progress as it does not align with trails strategy <i>Last Updated: 01-Jun-2022</i>				

Action Title: 9.1.5.35 HO7.5 Extend routes around the peat lakes for recreation.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	50%
Action Progress Comments: Lake Kainui walkway is now complete with access around the whole lake. Work is underway in an attempt to provide a similar asset at Rotokauri. <i>Last Updated: 30-May-2023</i>				

Action Title: 9.1.5.36 HO7.6 Improve the carpark at the bridge on Horotiu Bridge Road. Consider sealing it and adding toilets and rubbish bins.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Ongoing	01-Apr-2022	28-Feb-2023	-0%
Action Progress Comments: working with reserves team to complete works in year 3, this is a reserves project, but coordination between teams is required <i>Last Updated: 01-Jun-2022</i>				

2.3 Huntly

2.3.1 Communities

Action Title: 9.1.5.37 HU4.1 Prepare a reputational strategy that builds on local pride.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not yet started <i>Last Updated: 26-May-2022</i>				

Action Title: 9.1.5.38 HU4.2 Promote waka ama on the Waikato River and lakes.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not yet started <i>Last Updated: 02-Jun-2023</i>				

2.3.2 Economy

Action Title: 9.1.5.39 HU6.1 Promote a Puketirini and Kimihia (east mine) Employment, Skills and Technology Cluster that builds on existing uses (1).

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Ongoing	01-Jul-2021	30-Jun-2024	-0%
Action Progress Comments: Have Connected with Charlie Young, Jenifer, Murry, Greg Allen. <i>Last Updated: 12-May-2023</i>				

Action Title: 9.1.5.40 HU6.2 Promote a Puketirini and Kimihia (east mine) Building Fabrication Construction Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: <i>Last Updated: 25-Nov-2021</i>				

Action Title: 9.1.5.41 HU6.3 Continue to support the youth strategy to tie in with the development of the abovementioned proposed clusters (refer to HU6.1 and HU6.2).

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not yet started <i>Last Updated: 02-Jun-2023</i>				

Action Title: 9.1.5.42 HU6.5 Determine key town centre strategy and management needs (2).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2023	10%
Action Progress Comments: Council is scoping up work to determine opportunities to revitalise the Huntly Town Centre. This will connect in with other Capital works planned in and around the Township. <i>Last Updated: 30-May-2023</i>				

Action Title: 9.1.5.43 HU6.6 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the
Last Updated: 01-May-2023

Action Title: 9.1.5.44 HU6.4 Support the Huntly Wearable Arts event. Consider increasing its frequency and creating more economic spin-off (e.g. skills development).

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: In 2021 the Creative Communities Scheme and Huntly Community Board support this event. The event is held biannually and community led.
Last Updated: 26-May-2022

Action Title: 9.1.5.47 HU6.7 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 01-May-2023

2.3.3 Identity

Action Title: 9.1.5.45 HU1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Huntly, consider the lakes, power, mining, bricks, arts, and promote as a strong rugby league centre.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 02-Jun-2023

2.3.4 Nature

Action Title: 9.1.5.46 HU2.1 Prepare a strategy for the clean-up of the lakes and addressing any other environmental issues resulting from mining activity.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: This has not been planned for apart from minor planting and renewal of existing assets (walkways, park furniture etc)

Last Updated: 13-Jun-2023

2.3.5 Transport

Action Title: 9.1.5.48 HU7.1 Support the central interchange off the Waikato Expressway (watching brief).

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: There is no support from Waka Kotahi for a central interchange either in the vicinity of Kimihia Road or Mc Vie Road now that the Waikato Expressway has been completed. This was despite a 2017 report done by Aecom which recommended that a central interchange be constructed as part of the then NZTA's Waikato Expressway Huntly section contract works. A site visit was also undertaken by Mayor Allan, Cr Patterson, Cr Lynch and WDC and NZTA staff in 2020 during which our elected members advocated for an interchange. However Waka Kotahi has indicated that the case for an interchange does not stack up considering the agency's other priorities and funding constraints. Council and Waka Kotahi's focus is now on improving the Raahui Pookeka Huntly Railway Station. Staff recommend that the central interchange action be reconsidered by the Huntly Community Board since it is unlikely to get any traction.				
<i>Last Updated: 19-Apr-2023</i>				

Action Title: 9.1.5.49 HU7.3 Promote a new pedestrian river bridge (4).				
Responsible Person	Status	Start Date	End Date	% Complete
Rebecca Law - Reserves Planner	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: This is something for consideration as part of the Connectivity Strategy that is under development. Consideration will need to be given to see how this fits with the two existing pedestrian crossing point over the Waikato River.				
<i>Last Updated: 30-May-2023</i>				

Action Title: 9.1.5.50 HU7.2 Support the production of a cycle/walking strategy that links the lakes, river and town centre.				
Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jun-2022	30-Jun-2023	30%
Action Progress Comments: No specific cycle/walking strategy in the pipeline for Huntly. However we are currently developing the Connectivity Strategy which will incorporate aspirations for Huntly re. walking/cycling. We will be engaging with Community Boards during the consultation period of the strategy. Roading team working with Open Spaces Team to implement on-road walking links under LCLR Programme				
<i>Last Updated: 14-Jun-2023</i>				

2.3.6 Other

Action Title: 9.1.5.51 HU8.1 - Support the creation and implementation of a resource recovery centre				
Responsible Person	Status	Start Date	End Date	% Complete
Phillip Ellis - Solid Waste Team Leader	In Progress	01-Jul-2021	30-Jun-2024	25%
Action Progress Comments: Huntly - reconfiguration of site (capex component) to occur once Metrowaste has new recycling sorting plant built and operating at Rotowaro Rd site (imminent). Some delays on getting operating model and operator on site due to staffing/resource issues. Commercial model is for public drop off with external arrangements with others for supply/reuse of product. Some uncertainty re potential for dog pound being co-located at site.				
Tuakau - in detailed design phase. Multi-use site (solid waste, roading, dog pound satellite) at Bollard Rd which is greenfield site. Lags Huntly for implementation in LTP. Similar commercial model to Huntly but with Smart also co-located at site. Some issues re dog pound certainty but future proofing.				
<i>Last Updated: 25-May-2022</i>				

2.4 Matangi

2.4.1 Economy

Action Title: 9.1.5.53 MA6.1 Establish a Heritage, Cultural and New Economy Business Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	51%

Action Progress Comments: Matangi Heritage Committee is undertaking a cluster signage project to promote this activity.

Last Updated: 26-May-2022

Action Title: 9.1.5.54 MA6.2 Produce a village centre plan (1).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Matangi is not consider a growth node. At present Council does not have resource or budget allocated for a village centre plan. Priority could be considered as part of the 2024-2034 Long Term Plan. Donna has met with the Matangi Community Committee and talked though what the community could do themselves. An action was to circulate to the community some examples of Village Plans that could be used as a template.

Last Updated: 30-May-2023

Action Title: 9.1.5.55 MA6.3 Support landowners' initiatives to develop more mixed use and retail areas where deemed appropriate by the Council (2).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The Proposed District Plan Decision, supports mixed use development sought by local land owner.

Last Updated: 16-May-2022

Action Title: 9.1.5.56 MA6.4 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2024	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.57 MA6.5 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2021	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

2.4.2 Identity

Action Title: 9.1.5.52 MA1.1 Build on the strong identity of Matangi based on the unique qualities of the local area (refer to DW1.2 to 1.4). Consider the Matangi Factory history and current use.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: <i>Last Updated: 02-Dec-2021</i>				

2.4.3 Transport

Action Title: 9.1.5.58 MA7.1 Provide traffic calming and improved parking opportunities along the central section of Tauwhare Road.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jul-2024	30-Jun-2026	10%
Action Progress Comments: Deferred to next financial year due to late adoption of NZTA budgets <i>Last Updated: 14-Jun-2023</i>				

Action Title: 9.1.5.59 MA7.2 Construct a footpath along Matangi Road up to Fuchsia Lane (3), and create further connections to accommodate walking from the village centre to Hillcrest.

Responsible Person	Status	Start Date	End Date	% Complete
Grant J. Tregidga -	In Progress	01-Jul-2021	01-Mar-2022	80%
Action Progress Comments: matangi to fuschia lane complete <i>Last Updated: 14-Jun-2023</i>				

Action Title: 9.1.5.60 MA7.3 Implement a loop bus service through Matangi and Newstead.

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	In Progress	01-Jul-2021	30-Jun-2024	10%
Action Progress Comments: Waikato District Council and Waikato Regional Council have organised a workshop with both the Tamahere Community Committee and the Matangi Community Committee on 2 May to discuss the proposed bus service between Matangi, Tamahere and Hamilton. <i>Last Updated: 19-Apr-2023</i>				

2.5 Mercer

2.5.1 Communities

Action Title: 9.1.5.61 MC4.2 Consider the development of a community facility with a meeting place, possibly in the Fire Station (2). Consider incorporating public toilets.

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Negotiations continue with FENZ and owners of other buildings within Mercer but no definitive solution has been found.

Last Updated: 12-May-2023

Action Title: 9.1.5.62 MC4.1 Reconfigure the existing playground and upgrade playing fields.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: The current playground is a converted old tennis court. Land issues are being sorted where the playing fields are currently, and usage of fields also determines the need for upgrades -\$100,000 for playground, \$600,000 to upgrade playing fields. This doesn't include the clubrooms, which are in a state of disrepair. Discussions for associated Reserve Management Plan inclusion under Sports Park Reserve Management Plan for Mercer Domain once this process has been resolved. This will provide strategic direction for a reserve area.

Last Updated: 26-May-2022

2.5.2 Economy

Action Title: 9.1.5.63 MC6.2 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.64 MC6.3 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.65 MC6.1 Produce a village centre plan, placing an emphasis on destination, specialty retail and tourism, recreation, visitor and environmental aspects. Consider incorporating the relevant strategic opportunities proposed in the Local Area Blueprint.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Mercer is not consider a growth node. At present Council does not have resource or budget allocated for a village centre plan. Priority could be considered as part of the 2024-2034 Long Term Plan.

Last Updated: 30-May-2023

2.5.3 Identity

Action Title: 9.1.5.66 MC1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Mercer, consider tourism, wine, cheese, and skydiving.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 02-Jun-2023

2.5.4 Infrastructure

Action Title: 9.1.5.67 MC8.1 Consider providing appropriate facilities to address impact of freedom campers.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Needs clarification on the impact is from freedom camping in this community, whether there is a need for toilets, showers, bins, hardstand, dump station, BBQ facilities and shade. There is no current wastewater or water infrastructure. This would need to be factored into any budgets, as well as ongoing costs for maintenance and operation of these facilities. Land would be required for these facilities. \$750,000 land acquisition, \$1 million for double cubicle toilet, shower and sinks. Mercer does not have waters infrastructure so all facilities would need to be self sufficient with water supply and treatment of sewerage.

Last Updated: 26-May-2022

2.5.5 Iwi

Action Title: 9.1.5.68 MC3.1 Identify and preserve Maaori landmarks. Restore and commemorate historical Marae.

Responsible Person	Status	Start Date	End Date	% Complete
Ngahina Armstrong-Nield - Iwi and Community Partnerships Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 08-Dec-2021

2.5.6 Nature

Action Title: 9.1.5.69 MC2.1 Explore opportunities for wetland preservation and a park (1).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Area identified is subject to Treaty Settlement. This will have potential implications for all reserve areas north of Kimikimi Road. Staff awaiting direction from Crown on matter.

Last Updated: 26-May-2022

2.5.7 Transport

Action Title: 9.1.5.70 MC7.1 Increase parking and improve roading infrastructure. Consider a new overbridge and the relocation of the sliproad.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments: This project is not in current LTP

Last Updated: 01-Jun-2022

2.6 Meremere

2.6.1 Communities

Action Title: 9.1.5.71 MM4.1 Provide support to beautification initiatives, assisting with community pride in the place. Consider streetscape, entrance signs, house numbers etc.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	68%

Action Progress Comments: Meremere has started a letterbox beautification project. Supported by Spring Hill prison fund.

Last Updated: 26-May-2022

Action Title: 9.1.5.72 MM4.2 Leverage more activities off the Hall. Seek sponsorship, e.g. for heating (considering solar power) and equipment (2).

Responsible Person	Status	Start Date	End Date	% Complete
Tracey Morgan - Acting Facilities Team Leader	Ongoing	01-Jul-2021	30-Jun-2024	-0%

Action Progress Comments: WDC have employed a Halls officer who are able to support Hall committees throughout the district to undertake these types of activities.

Last Updated: 12-May-2023

Action Title: 9.1.5.73 MM4.3 Prepare a community engagement framework describing how to enable new initiatives, and strengthening relationships between existing committees and the community.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	2%

Action Progress Comments: Currently in discussion with various committees

Last Updated: 26-May-2022

Action Title: 9.1.5.74 MM4.4 Prepare a reputational strategy that builds on local pride.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

Action Title: 9.1.5.75 MM4.5 Develop youth engagement initiatives to address the issue of youth leaving school early.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

Action Title: 9.1.5.76 MM4.6 Consider ways to provide more recreational opportunities and facilities for children.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	70%

Action Progress Comments: New playground and skatepark under way which will provide these activities. Council led with community engagement. (CAMMS PR-21319).

Last Updated: 12-May-2023

2.6.2 Economy

Action Title: 9.1.5.77 MM6.1 Prepare an employment strategy for rangitahi that supports TGH efforts (3).

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	1%

Action Progress Comments: Workforce development a priority in ED new work program .

Last Updated: 12-May-2023

Action Title: 9.1.5.78 MM6.4 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.79 MM6.5 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.80 MM6.2 Establish a Synergy Park / Clean Production cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 09-Dec-2021

Action Title: 9.1.5.81 MM6.3 Establish a High Performance Vehicle Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	1%

Action Progress Comments: Discussions in place with Hampton downs and Meremere speedway to work in collaboration and potentially expand operations.

Last Updated: 12-May-2023

2.6.3 Identity

Action Title: 9.1.5.82 MM1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Meremere, consider the power station, motorsport, and Whangamarino wetlands.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%
Action Progress Comments: Not yet started				
<i>Last Updated: 26-May-2022</i>				

2.6.4 Iwi

Action Title: 9.1.5.83 MM3.1 Celebrate the Redoubt, linking it to a wider Maori heritage experience (Tuakau, Pokeno, to Rangiriri etc) (1). Add some associated commercial zoning.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Ongoing	01-Jul-2021	30-Jun-2022	-0%
Action Progress Comments: The ramparts and trenches that formed the core of the Rangiriri Pa's defences are ready, and the reconstructed North Waikato pa formally re-opened on 23 April 2022. Further Community Led projects could be done to connect to Meremere, Mercer, Pokeno and Tuakau as part of the Land Wars story. Consideration for additional Commercial Land Use has not yet been undertaken.				
<i>Last Updated: 30-May-2023</i>				

2.6.5 Transport

Action Title: 9.1.5.84 MM7.1 Support continued access off the Waikato Expressway.

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	In Progress	01-Feb-2022	30-Jun-2023	50%
Action Progress Comments: The main focus for Council staff at present in so far as access to the Expressway is concerned, relates to to the Meremere A industrial area. The strategic issue at Meremere for Tainui Group Holdings (administer the land on behalf of the tribe) is eventually unlocking the development of Meremere A for a major recycling centre of excellence notwithstanding the infrastructure challenges. This is the long-term outcome that TGH aspires to. TGH and WDC have held joint meetings with Waka Kotahi to explore options for the short term and long-term access to the Waikato Expressway from Meremere A. Waka Kotahi has advised TGH that resource consent will be required as a restricted discretionary activity under Rule TRPT-R4 (Traffic Generation) of the Proposed Waikato District Plan- Decisions Version, due to the number of heavy vehicles proposed for access in and out of the site. There are currently safety challenges at the Island Block Road/State Highway 1 intersection. Specifically, in relation to HCV's using the left turn slip lane into Island Block Road as this will obscure visibility to those trying to exit Island Block Road.				
Waka Kotahi wants to understand the adverse effects on the Island Block Road/State Highway 1 intersection because of the additional heavy vehicle movements. This would best be done in the form of an Integrated Transport Assessment (ITA). Once a traffic engineer has been engaged by TGH, Waka Kotahi will organise a meeting prior to an ITA being undertaken to discuss the scope/methodology of the ITA contents.				
<i>Last Updated: 19-Apr-2023</i>				

Action Title: 9.1.5.85 MM7.2 Consider an overbridge that also allows access to the river and Te Araroa Trail.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%
Action Progress Comments: This project is not in current LTP				
<i>Last Updated: 01-Jun-2022</i>				

2.7 Ngaruawahia

2.7.1 Communities

Action Title: 9.1.5.86 NG4.1 Undertake strategic conversations around Council-owned land and halls for reinvigoration of community assets (1).

Responsible Person	Status	Start Date	End Date	% Complete
Michelle Brown - Acting Strategic Property Manager	In Progress	01-Jul-2021	30-Jun-2024	23%

Action Progress Comments: Update from Cr Gibb 18/7/22:
Last Updated: 26-May-2023

Action Title: 9.1.5.87 NG4.2 Produce a planting plan and social space at Te Mana o te Rangi reserve (2).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	50%

Action Progress Comments: Ngaruawahia Community Board and WDC staff have developed this in conjunction. Signs installed to identify the site - complete.
Last Updated: 26-May-2022

Action Title: 9.1.5.88 NG4.3 Work with relevant entities to support the strategy for youth initiatives.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started.
Last Updated: 02-Jun-2022

Action Title: 9.1.5.89 NG4.4 Address freedom camping issues.

Responsible Person	Status	Start Date	End Date	% Complete
Tanya O'Shannessey - Monitoring Team Leader	In Progress	01-Jul-2021	30-Jun-2024	1%

Action Progress Comments: Compliance monitoring ongoing - often in partnership with Reserves Team. Freedom Camping Bylaw 2016 will commence its review in Nov/Dec 2022 with a focus on increased signage, assessment of problem areas and a strong connectedness to the Reserves Bylaw. Particular attention to be paid to Freedom Camping hotspots in Ngaruawahia.
Last Updated: 27-Apr-2022

2.7.2 Economy

Action Title: 9.1.5.90 NG6.1 Undertake initiatives to ensure tidy commercial and industrial street frontages.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Roller door project underway. Clean and re- instate murals on shop frontages along Great South rd. Ngaruawahia Community Board initiative with WDC support.
Last Updated: 31-May-2022

Action Title: 9.1.5.91 NG6.4 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	40%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.92 NG6.5 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Sep-2023	40%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

The Ngaruawahia Structure Plan is currently underway and will look at all land use within the Ngaruawahia community.

Last Updated: 30-May-2023

Action Title: 9.1.5.93 NG6.2 Promote water based recreation opportunities, including the development of a café (4).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2022	40%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the

Last Updated: 30-May-2023

Action Title: 9.1.5.94 NG6.3 Promote the idea of recreational opportunities in and around the Hakarimata Ranges, consider a gondola or a waterslide (5).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Not Started	01-Jul-2021	30-Jun-2022	0%

Action Progress Comments: The Hakarimata Ranges is a sensitive natural environment and promotion of a gondola or waterslide could have a negative impact on the natural environment.

Last Updated: 30-May-2023

2.7.3 Growth

Action Title: 9.1.5.95 NG5.1 Consider extending the business zone (see strategic opportunities diagram) (3).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Sep-2023	40%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the

Last Updated: 30-May-2023

2.7.4 Identity

Action Title: 9.1.5.96 NG1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Ngaruawahia, consider Te Kiingitanga, the confluence of the Waipa and Waikato Rivers, and the Hakarimata Ranges.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

Action Title: 9.1.5.97 NG1.2 Erect signage at the six entry points into Ngaruawahia, refer to its unique local identity and to promote tourism (also refer to NG1.1).

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Dec-2021

2.7.5 Infrastructure

Action Title: 9.1.5.98 NG8.1 Install or upgrade toilet facilities (11).

Responsible Person	Status	Start Date	End Date	% Complete
Megan May - Acting General Manager - Service Delivery	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Toilets at The Point Reserve have been upgraded and new toilets have been installed at Centennial Park. No other toilets identified for installation in Ngaruawahia

Last Updated: 01-Jun-2022

2.7.6 Iwi

Action Title: 9.1.5.99 NG3.1 Promote local cultural tourism by local iwi (also refer to DW1.4).

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	1%

Action Progress Comments: Discussions started with Tainui Waka Tourism inc to promote tourism through our Open Waikato brand.

Last Updated: 12-May-2023

2.7.7 Nature

Action Title: 9.1.5.100 NG2.1 Undertake a pest control project in the Hakarimata Ranges. Consider this as an opportunity for a community-led conservation project (also refer to DW2.1).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Hakarimata Range is managed by Department of Conservation. Waikato District Council owns a very small portion. DoC is keen to engage the community in projects like this.

Last Updated: 01-Jun-2022

2.7.8 Transport

Action Title: 9.1.5.101 NG7.3 Provide longer distance walking and cycling connections to Te Otamanui (7), Glen Massey (8), the eastern side of the Waikato River to Horotiu (9), and Taupiri (10) (also refer to DW1.3).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments: This project is not in current LTP, no projects in the trail strategy for these locations

Last Updated: 01-Jun-2022

Action Title: 9.1.5.102 NG7.2 Investigate opportunities for traffic calming and speed reductions on Great South Road through the town centre and for improved east-west connectivity for pedestrians and cyclists (6).

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments: This project is not in current LTP, this is being developed as part of the structure plan 2024/26 LTP
Last Updated: 01-Jun-2022

Action Title: 9.1.5.103 NG7.1 Upgrade pedestrian connections in the town centre and to the Te Awa river ride.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments:
Last Updated: 13-Dec-2021

2.8 Ohinewai

2.8.1 Communities

Action Title: 9.1.5.106 OH4.1 Review accessibility to / for emergency services.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Dec-2021

Action Title: 9.1.5.107 OH4.2 Support community initiatives for an area tidy up, addressing rubbish and weeds.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started.

Last Updated: 14-Jun-2023

Action Title: 9.1.5.108 OH4.3 Extend the Council's fruit tree planting programme.

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: This is underway in other parts of the district. It is community led but Council's Events team is happy to facilitate this.

Last Updated: 01-Jun-2022

Action Title: 9.1.5.109 OH4.4 Undertake the paint initiative for 'Cowboys'.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Dec-2021

Action Title: 9.1.5.110 OH4.5 Assist with the set up of social media and website communications within the community.

Responsible Person	Status	Start Date	End Date	% Complete
Emma Edgar - Executive Manager - Communications & Engagement	In Progress	01-Jul-2021	30-Jun-2024	50%

Action Progress Comments: A guideline/ toolkit is being developed to provide branding and content strategy advice and will be used to provide a framework for others who are keen to explore digital communications options. In

Last Updated: 14-Jun-2023

Action Title: 9.1.5.111 OH4.6 Provide Council support to local events.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	90%

Action Progress Comments: Community run events happening on Council land are processed through our Events Officer.

Last Updated: 01-Jun-2022

Action Title: 9.1.5.112 OH4.7 Support the expansion of the school and increase in childcare provision. Consider whether the hall can double.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Dec-2021

2.8.2 Growth

Action Title: 9.1.5.113 OH5.1 Investigate the potential for larger residential lots west of SH1, and a mix of larger and smaller lots (for affordability) east of SH1.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: There is a small allowance for large lot residential on the western side of SH1. The Proposed District Plan Decision provides for residential development on the eastern side of SH1.

Last Updated: 17-May-2022

Action Title: 9.1.5.114 OH5.2 If development application progresses, then ensure possible expansion addresses its own impacts (such as traffic, noise, and visual). Ensure it contributes positively to the local community, e.g. by offering more convenience retail, improving housing affordability, new walking and cycling connections, improving the viability of the school etc. (2)

Responsible Person	Status	Start Date	End Date	% Complete
Sandra Kelly - Programme Manager District Plan	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments:

Last Updated: 12-May-2022

2.8.3 Identity

Action Title: 9.1.5.104 OH1.1 Build a strong identity based on a village community, river corridor, and the unique qualities of the local area (refer to DW1.1 to 1.4). For Ohinewai, consider the ferry landing.

Responsible Person	Status	Start Date	End Date	% Complete
Lianne Van Den Bemd - Community Led Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments: Not yet started

Last Updated: 26-May-2022

2.8.4 Infrastructure

Action Title: 9.1.5.119 OH8.1 Insert fibre with other services.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	30%

Action Progress Comments: Cr Whyte reports that fibre has been laid at Ohinewai North and South Roads and vicinity, due to planned Sleepyhead Development. Therefore in progress.

Last Updated: 14-Jun-2023

2.8.5 Nature

Action Title: 9.1.5.105 OH2.1 Clarify the future of the reserve (1).

Responsible Person	Status	Start Date	End Date	% Complete
--------------------	--------	------------	----------	------------

Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	80%
Action Progress Comments: Natural Reserve Management Plan was adopted in December 2018. Staff to execute actions identified within this document. Lake Ohinewai ecological enhancement and access project underway.				
Cr Whyte's understanding is that this has been clarified and this action could be considered completed.				
<i>Last Updated: 14-Jun-2023</i>				

2.8.6 Transport

Action Title: 9.1.5.115 OH7.1 Create tracks on the stop bank along the Waikato River and around Lake Ohinewai (3).				
Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	In Progress	01-Jul-2022	30-Jun-2024	5%
Action Progress Comments: WORKING WITH DEVELOPER ON THE SLEEPYHEAD PROGRAMME				
<i>Last Updated: 14-Jun-2023</i>				

Action Title: 9.1.5.116 OH7.1a Create tracks on the stop bank along the Waikato River				
Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2022	30-Jun-2024	5%
Action Progress Comments: WORKING WITH SLEEPERHEAD DEVELOPEMENT ON THIS				
<i>Last Updated: 02-Jun-2022</i>				

Action Title: 9.1.5.117 OH7.1b Create tracks around Lake Ohinewai (3).				
Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	80%
Action Progress Comments: Lake Ohinewai ecological enhancement and access project underway.				
<i>Last Updated: 14-Jun-2023</i>				

Action Title: 9.1.5.118 OH7.2 Add a pedestrian/cycling 'clip-on' onto the Tahuna Road bridge over the railway and over SH1 (4).				
Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Deferred	01-Jul-2022	30-Jun-2024	1%
Action Progress Comments: This project is not in current LTP and will be part of future consents for Sleepyhead development providing a separate pedestrian bridge				
<i>Last Updated: 01-Jun-2022</i>				

2.9 Pokeno

2.9.1 Communities

Action Title: 9.1.5.22 PO4.1 Consider the need for a sports park. Consider whether Munro Reserve can be improved for this or whether the park in the western growth area can be expanded (1).

Responsible Person	Status	Start Date	End Date	% Complete
Glyn Morgan - Open Spaces Team Leader & Acting Team Leader Reserve Planning	In Progress	01-Jul-2021	30-Jun-2024	55%
Action Progress Comments: Initial earthworks of Munro Park completed. Further earthworks happening next Summer to prepare site for development. Draft concept plan developed and socialised with community. More in depth community engagement planned to confirm details of each asset - playground, skatepark/pump track etc.				

Last Updated: 12-May-2023

Action Title: 9.1.5.23 PO4.2 Establish library, community and customer services and / or facilities.

Responsible Person	Status	Start Date	End Date	% Complete
Shelby Spain - Customer Delivery Manager	In Progress	01-Jul-2021	30-Jun-2024	10%
Action Progress Comments: Currently in the EPMO space & Facilities				

Last Updated: 26-May-2023

Action Title: 9.1.5.120 PO4.3 Work with MOE to provide adequate schooling facilities for the current and future population.

Responsible Person	Status	Start Date	End Date	% Complete
Julie Dolan - Economic and Community Development Manager	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Dec-2021

2.9.2 Economy

Action Title: 9.1.5.123 PO6.1 Prepare a detailed retail needs calculation, preliminary transport and open space options (4), followed by the production of a town centre strategy that reconciles the current and future retail, employment, community facility, and open space needs.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jul-2021	30-Jun-2022	85%

Action Progress Comments: The Pokeno Public Realm Concept Plan was adopted by Council on 11 May 2022. This identifies public space, open space connections, transport links and urban form for the Pokeno Town Centre. The retail needs assessment is the remaining outstanding piece of work to be completed.

Last Updated: 17-May-2022

Action Title: 9.1.5.124 PO6.2 Establish an Advanced Food Processing Cluster.

Responsible Person	Status	Start Date	End Date	% Complete
Kelvin Forsman - Economic Development Advisor	Not Started	01-Jul-2021	30-Jun-2024	0%

Action Progress Comments:

Last Updated: 13-Dec-2021

Action Title: 9.1.5.125 PO6.3 Identify if, how much, and where, possible additional employment land for office development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

Last Updated: 30-May-2023

Action Title: 9.1.5.126 PO6.4 Identify if, how much, and where, possible additional employment land for retail development is needed beyond the zoning in the Proposed District Plan.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	In Progress	01-Jun-2022	30-Sep-2023	20%

Action Progress Comments: The Business Assessment (part of the Housing and Business Assessment as required under the NPS-UD) update is currently underway by the Future Proof partnership and expected to be completed by the end of June 2023. This will determine if there is a shortfall or not of Employment land. Employment land includes industry, commercial and retail which result in the following district plan zones (Industrial, Town Centre, Commercial and Local Centre zones).

The Ngaruawahia Structure Plan is currently underway and will look at all land use within the Ngaruawahia community.

Last Updated: 30-May-2023

2.9.3 Growth

Action Title: 9.1.5.121 PO5.1 Consider support residential expansion (2).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: The Proposed District Plan Decision allows for additional residential development in several areas across the township.

Last Updated: 17-May-2022

Action Title: 9.1.5.122 PO5.2 Consider supporting the Village Zone expansion (3).

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Completed	01-Jul-2021	30-Jun-2022	100%

Action Progress Comments: Village zoning (now called large lot residential) is not supported in townships as it does not deliver on our density targets. A new Future Urban Zone area was identified in the Proposed District Plan Decisions on the western side of the Pokeno township adjacent to the existing large lot residential zone.

Last Updated: 17-May-2022

2.9.4 Identity

Action Title: 9.1.5.21 PO1.1 Build a strong identity based on the river corridor, and the unique qualities of the local area.

Responsible Person	Status	Start Date	End Date	% Complete
Jason Marconi - Economic Development Advisor	In Progress	01-Jul-2021	30-Jun-2024	11%

Action Progress Comments: Pokeno Community Committee have approached WDC for funding for community website.

2.9.5 Transport

Action Title: 9.1.5.127 PO7.1 Investigate establishing wider transport links with employment areas, Tuakau and SH1. Consider a new underpass and / or bypass.

Responsible Person	Status	Start Date	End Date	% Complete
Grant Tregidga - Roading Manager	Not Started	01-Jul-2024	30-Jun-2026	0%

Action Progress Comments: Long-term project not in current LTP and will be developed as part of the structure plan for the next LTP

Last Updated: 01-Jun-2022

Action Title: 9.1.5.128 PO7.2 Work with the truck stop owner to address community concerns.

Responsible Person	Status	Start Date	End Date	% Complete
Donna Tracey - Strategic Planning Manager	Ongoing	01-Jul-2021	30-Jun-2022	-0%

Action Progress Comments: Council has had several conversations with the owner of the land where the truck stop is located in relation to proposed upgrades to Great South Road.

Last Updated: 30-May-2023

Action Title: 9.1.5.129 PO7.3 Create a Park and Ride for public transport

Responsible Person	Status	Start Date	End Date	% Complete
Vishal Ramduny - Strategic Initiatives and Partnership Manager	In Progress	01-Jul-2024	30-Jun-2026	50%

Action Progress Comments: Council currently owns land for a future railway station at Pokeno. There is an opportunity for a park and ride facility associated with this. Preliminary staff assessment indicates that, besides a railway platform, the land can accommodate about 60 car parking spaces and 4 bus layovers. However, there is currently no funding in the current (2021-2031) LTP for construction of either the railway platform or the park and ride facility. Any future location of a railway station here would need to be assessed against having one in Tuakau and Te Kauwhata - with consideration given to both short and long term benefits of the location as well as costs. This is work that is currently underway through the development of an indicative business case (feasibility study) to consider the most feasible location of a potential railway station in the northern Waikato. This work is expected to be completed at the end of June 2023. A detailed business case (for which there is no committed funding) will then have to be done for a potential station. Funding for the detailed business case will be a matter for consideration in the 2024-2034 LTP. The construction of a second passenger railway station in the district is subject to government funding and partnership support as this cannot be solely ratepayer funded.

Last Updated: 19-Apr-2023

